

Facility Management Department**SOP Title: FM_SOP****Facilities Management****Process Standards****SOP Number: FM_Fulfillment_01_26****SOP Title: FM SOP**

	Name	Title	Signature	Date
Author	Mostafa Magd	Manager, Facilities		
Reviewer				
Authorizer				

Effective Date:	
Review Date:	

READ BY			
NAME	TITLE	SIGNATURE	DATE

1. Purpose

Facility Management Standard Operating Procedures “FM SOP” is a document that contains a detailed set of instructions that outlines how a business needs to be operated. The aim of this document is to describe the step-by-step process that must be taken to properly perform a routine activity. In this document, you will find the policies, processes and standards needed to put the team in one track and ensure consistency and stability in team’s performance which will lead the team to perform in the same way. This will benefit the business and the team to avoid any deviations, reduce errors and risks, increase efficiencies and profitability, create a safe work environment, and produce guidelines for how to resolve issues and overcome obstacles.

Table of Contents

1. PURPOSE.....	2
2. INTRODUCTION.....	8
3. FACILITY MANAGEMENT (FM).....	8
3.1 FM'S ADDING VALUE.....	8
3.2 FM'S ORGANIZATIONAL STRUCTURE.....	10
3.3 FM'S ORGANIZATIONAL STRUCTURE CHART.....	11
3.4 FM'S SCOPE AND FIELDS.....	12
3.5 FM'S SCOPE AREA AND BOUNDARIES.....	13
3.6 FM'S RESPONSIBILITIES AND RESOURCES ALLOCATION.....	14
3.7 FM'S KPIS.....	19
3.8 FM'S DELEGATION OF AUTHORITY (DOA).....	20
3.9 FM'S WORKING HOURS AND WEEK-OFFS.....	27
3.10 FM'S REGULATIONS AND POLICES.....	28
4. FM'S STANDARD OPERATING PROCEDURE (SOP).....	29
4.1 TICKETING.....	29
4.1.1 FACILITY MANAGEMENT TICKET (FM TICKET).....	29
4.1.2 TICKETING SYSTEM.....	30
4.1.3 FM TICKET CYCLE AND PROCESS.....	30
4.1.4 FM TICKET FLOW CHART.....	32
4.1.5 FM TICKET STATUS DEFINITION.....	33
4.1.6 FM TICKET POLICY.....	33
4.1.7 FM TICKET ASSIGNING AND DELEGATION.....	34
4.1.8 FM TICKET APPROVERS MATRIX.....	35
4.1.9 FM TICKET CLASSIFICATION.....	35
4.1.10 FM TICKET COMMUNICATION MATRIX.....	36
4.1.11 FM TICKET TIMELINE.....	38
4.1.12 FM TICKET CRITERIA.....	40
4.1.13 PROCUREMENT TICKETS (PR TICKETS).....	40
4.1.14 PO TOOL REQUESTS.....	42
4.1.15 FINANCE TICKETS (PAYMENT REQUESTS).....	42
4.2 PROJECT MANAGEMENT.....	45

4.2.1 PROJECTS SCOPE OF WORK.....	45
4.2.2 PROJECTS CLASSIFICATION.....	46
4.2.3 PROJECT MANAGEMENT PROCESS.....	46
4.2.4 NEW FACILITY SCOUTING & PREPARATIONS.....	50
4.2.5 CLOSING & EVACUATING FACILITY.....	51
4.3 SCRAP MANAGEMENT.....	54
4.3.1 SCRAP DEFINITION.....	54
4.3.2 OPERATION DISPOSAL.....	54
4.3.3 GENERAL SCRAP.....	54
4.3.4 ENVIRONMENTALLY HARMFUL SCRAP.....	54
4.3.5 DISPOSAL PROCESS AND POLICY.....	55
4.3.6 SCRAP PROCESS AND POLICY.....	57
4.3.7 SCRAP COLLECTION FREQUENCY.....	58
4.4 SOFT FACILITY MANAGEMENT (SFM).....	59
4.4.1 HOUSEKEEPING SERVICES (HK SERVICES).....	59
4.4.2 PEST CONTROL SERVICES.....	65
4.5 VENDOR MANAGEMENT.....	68
4.5.1 VENDOR LIST AND CLASSIFICATION.....	69
4.5.2 VENDOR MANAGEMENT PROCESS AND POLICY.....	72
4.5.3 IN-HOUSE SCOPE VS OUTSOURCE SCOPE.....	73
4.5.4 VENDORS KEY PERFORMANCE INDICATORS (VENDORS' KPIS).....	76
4.6 ASSET MANAGEMENT.....	81
4.6.1 ASSET REGISTER.....	81
4.6.2 ASSET TAGGING.....	81
4.6.3 ASSET TRANSFERS.....	86
4.6.4 ASSET STOCK-TAKE.....	87
4.6.5 ASSET MANAGEMENT POLICY.....	87
4.7 DOCUMENTATION.....	88
4.7.1 FM LEAVES AND ATTENDANCE.....	88
4.7.2 DAILY REPORT.....	91
4.7.3 CHECKLISTS.....	91
4.7.4 ATTENDANCE.....	92

5. CATERING SERVICES PROCEDURE.....	93
5.1 ROUTINE / DAY-TO-DAY CATERING.....	93
5.2 EVENT / MEETING CATERING REQUESTS.....	93
5.3 VENDOR MANAGEMENT.....	93
5.4 QUALITY, HYGIENE & FOOD SAFETY.....	93
5.5 INVOICING, PAYMENT & RECONCILIATION.....	93
5.6 RECORDS & DOCUMENTATION.....	94
6. COURIER SERVICES PROCEDURE.....	95
6.1 REQUEST INITIATION.....	95
6.2 APPROVAL & SPEND THRESHOLDS.....	95
6.3 DISPATCH.....	95
6.4 COST CONTROL & INVOICING.....	95
6.5 RECORDS & DOCUMENTATION.....	95
7. APPROVAL MATRIX & SPEND THRESHOLDS.....	96
8. SITE COORDINATION.....	97
9. EXCEPTIONS & EMERGENCY PROCEDURES.....	97
10. NON-COMPLIANCE & ESCALATION.....	97
11. INTERNAL AND EXTERNAL REFERENCES.....	98
11.1 INTERNAL REFERENCES.....	98
11.2 EXTERNAL REFERENCES.....	98
12. FACILITIES DETAILS.....	99
12.1 LAYOUTS AND DESIGNS.....	99
13. RECOMMENDATIONS.....	100
13.1 COMPUTERIZED MAINTENANCE MANAGEMENT SYSTEM - CMMS.....	100
14. CHECKLISTS TEMPLATES.....	101
14.1 FM TECHNICIANS DAILY REPORT.....	101
14.2 DAILY UTILITY INSPECTION CHECKLIST.....	103
14.3 FM HK CHECKLIST.....	104
14.4 FM STOCK CONSUMPTION REPORT.....	105

14.5 VENDOR EVALUATION TEMPLATE.....	108
14.6 FACILITY HANDOVER.....	109
15. DEFINITIONS AND ABBREVIATIONS.....	114
16. CHANGE HISTORY.....	116

LIST OF TABLES

Table 1 - Scope Areas.....	13
Table 2 - FM's Responsibilities and Resources Allocation.....	14
Table 3 - FM's KPIs.....	19
Table 4 - FM's Delegation of Authority Matrix.....	20
Table 5 - FM's Working Hours and Week-offs.....	27
Table 6 - FM Ticket Approvers Matrix.....	35
Table 7 - FM Ticket Classification.....	36
Table 8 - FM Ticket Communication Matrix.....	36
Table 9 - FM Ticket Timeline.....	39
Table 10 - Projects Classification.....	46
Table 11 - Housekeeping Headcount and Manpower Distribution.....	63
Table 12 - Pest Control Scope.....	65
Table 13 - Pest Control Penalty Matrix.....	66
Table 14 - Vendor List and Classification.....	69
Table 15 - Contractual Vendor Evaluation Criteria.....	76
Table 16 - Vendors Rating Scale.....	78
Table 17 - Vendors' KPIs.....	79

Table 18 - Vendors Rating Scale.....	80
Table 19 - Asset Tagging Guidance - Country Code.....	81
Table 20 - Asset Tagging Guidance - Asset Category.....	81
Table 21 - Asset Tagging Guidance - Fixed Assets.....	81
Table 22 - Type of Leaves.....	88
Table 23 - Checklist Schedule.....	91
Table 24 - Designs and Layouts.....	99
Table 25 - FM Technicians Daily Report.....	101
Table 26 - Daily Utility Inspection Checklist.....	103
Table 27 - HK Checklist.....	104
Table 28 - Stock Consumption Report.....	105
Table 29 - Vendor Evaluation Template.....	108
Table 30 - Definitions and Abbreviations.....	114

List of Figures

Figure 1 - FM Ticket Process Flow Chart.....	32
Figure 2 - Project Management Process (PMI).....	47
Figure 3 - Screenshot for FM Stock Sheet.....	75

2. Introduction

“FM SOP” is the key to maintaining trust and confidence between the FM Team and other functions. “FM SOP” is a set of

guidelines that keep our job expectable, smooth &, more important, consistent.

To put the guidelines that maintain consistency in performance, it is vital to understand the job nature of the FM Team:

3. Facility Management (FM)

According to the IMFA, *“Facility Management (FM) is a profession dedicated to supporting people. It ensures the functionality, comfort, safety, sustainability, and efficiency of the built environment - the buildings we live and work in and their surrounding infrastructure”*

Facility Management is an organizational function which integrates people, place, and process within the built environment with the purpose of improving the quality and productivity of the core business.

This combination of job responsibilities supports the operations of each organization to create an environment where the systems work together seamlessly, from the parking lot to the executive suite. Facility managers are the people who make sure we have the safest and best experience possible, by coordinating the processes that make the built environment succeed.

3.1 FM's Adding Value

FM touches every part of the business. In focusing on these vital aspects of facilities, businesses gain powerful benefits that translate into value-adds at every level of operation. Here's a look at some of the most important:

- Reduces operational costs
- Enhances safety, security, and preparedness
- Improves organizational culture
- Implements value engineering


- Supports decision making
- Acknowledges business needs
- Contributes to achieve the business goals
- Maintains smooth and unstoppable core operations
- Maintains corporate's assets
- Works on energy saving and rationalization
- Maintains environmental sustainability
- Optimizes the space and occupancy

3.2 FM's Organizational Structure

FM Team can be defined as the tools and services that support the functionality, safety, and sustainability of buildings, operations, and infrastructure. FM Team contributes to your organization's bottom line, impacting the short- and long-term value of property, buildings, assets, and equipment. Behind this noble mission, there are **nine** heroes who invest their efforts, time, knowledge and focus to achieve the stability, consistency, and growth to the business:

- Director
- Manager
- Supervisor
- Admin Senior Colleague
- Technician
- 4 Admin Colleagues

3.3 FM's Organizational Structure Chart

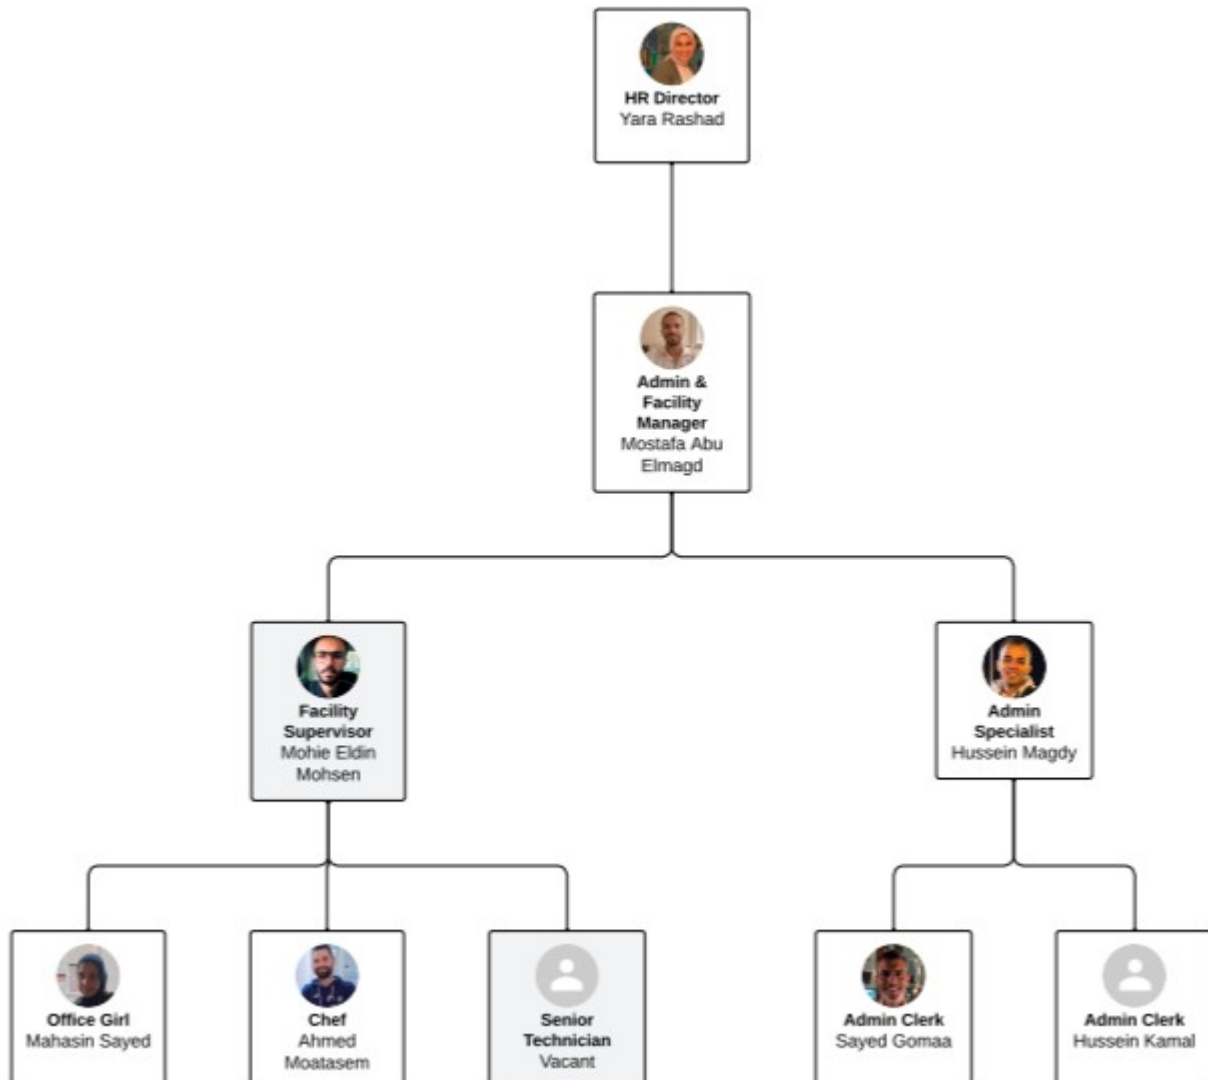

3.4 FM's Scope and Fields

Also, here are the fields that the FM Team covers in the scope:

- Strategic planning
- Project management
- FM ticket callouts responding
- Maintenance works
- Breakdown management
- Electricity works
- Piping works
- Mechanical works
- Drainage works
- Construction works
- In-house installation works
- Finance works
- Material selections and BOQs preparations
- Planned preventive maintenance (PPM)
- Periodic tests
- Asset management
- Scrap management
- Scouting
- Energy Management
- Catering
- Courier service

3.5 FM's Scope Area and Boundaries

FM Team's scope covers the following facilities:

Table 1 - Scope Areas

Sites	Locations	Adress	POC
Arkan Mall PV	https://maps.app.goo.gl/9xgHMTyvCg1VzbeY7	Sheikh Zayed City	Abd ElRahman Medhat
Orion Factory	https://maps.app.goo.gl/MJ5Yfzww2QBGDRza9	6th October City	Abd ElRahman Medhat
Mazar Mall PV	https://maps.app.goo.gl/5MM4geFrWDGSqhWbA	Sheikh Zayed City	Abd ElRahman Medhat
C3A	https://maps.app.goo.gl/KSH4hcKaH1C62rXj8	Wahat	Islam Gomaa
Juhaina	https://maps.app.goo.gl/8rwp78BqeJNti2wm7	Wahat	Islam Gomaa
Abu Monkar	https://maps.app.goo.gl/poRM6LSRAFSMvCL96	Abu Monkar - Farafra	Ahmed El-Soghayer
DAK-01	https://maps.app.goo.gl/1cH8CkeLUK74FNiR9	Minya	El Sayed Shahin
DAK-02	https://maps.app.goo.gl/ikbWsEmuDoNNmGm67	Wadi Elnatroon	Mohamed El-Sholhy
Sahl Hashish	https://maps.app.goo.gl/oTNaDEiA7fN6xpYW8	Sahl Hashish	Omar Hashish
Oasis	https://maps.app.goo.gl/LhUDuJQufds3H2PA7	North Marsa Alam	Omar Hashish
Equinox	https://maps.app.goo.gl/ci9SA8YZruK4mVCC8	North Marsa Alam	Omar Hashish
Marsa Shagara	https://maps.app.goo.gl/Csp6gukoeFd2jrAAA	North Marsa Alam	Omar Hashish
Lahmy Bay	https://maps.app.goo.gl/gbmVi3wriqAhBCYh8	South Marsa Alam	Omar Hashish
Wadi Lahmy Azure	https://maps.app.goo.gl/WTGJVasbmGQXXnyz8	South Marsa Alam	Omar Hashish
Nakari	https://maps.app.goo.gl/WN8xXUkMfHqCtjkBA	South Marsa Alam	Omar Hashish
Wadi Lahami	https://maps.app.goo.gl/VZFEE83Athr6kBfp8	South Marsa Alam	Omar Hashish
District 5	https://maps.app.goo.gl/mTSnsVkefqyHkScB8?g_st=a	New Cairo	Mohamed Hesham

3.6 FM's Responsibilities and Resources Allocation

As listed in the "FM's Scope and Fields" section, FM Team covers several fields using the available manpower resources. In the below table, responsibilities will be described in respect to the manpower and task owners (primary and secondary):

Table 2 - FM's Responsibilities and Resources Allocation

i	Scope	Description	Primary Task Owner	Secondary Task Owner
1	Strategic Planning	- Identify corporate's goals - Plan for the future - Define milestones and deliverables - Prepare timelines and schedules - Monitor team's performance - Communicate with top management and other functions	Manager	Supervisor
2	Project management	- Initiate the project process - Plan for the project timeline, resources needed, budgets & material needed - Execute the project according to the timeline and specs. Monitor the project's progress - Close the project	Manager	Supervisor

i	Scope	Description	Primary Task Owner	Secondary Task Owner
3	FM ticket callouts responding	- Respond to other function's callouts - Understand requester's requirements Ensures that requirements are delivered to the requester on time	Manager	Supervisor and Senior Admin Lead
4	Maintenance works	- Ops tools and equipment maintenance - Small Items repairing and fixing - Air conditioning maintenance - General renovation works	Outsourced Vendors	FM Technician
5	Breakdown management	- ACs maintenance - Office Printers breakdown	Outsourced Vendors	FM Technician

i	Scope	Description	Primary Task Owner	Secondary Task Owner
6	Electricity works	• Powering • Lighting • Emergency lines connections • Load balancing • Controls • Energy saving tools (timers, motion sensors)	FM Technician	Outsourced Vendors
7	Piping/ Plumbing works	• Firefighting network installations • Fire alarm system installations • Drainage network installations	Outsourced Vendors	FM Technicians
8	Mechanical works	• Ops machines' components installation and dismantling	FM Technicians	Outsourced Vendors

i	Scope	Description	Primary Task Owner	Secondary Task Owner
9	Drainage works	• Drainage pipe unblocking and fixation • Bathrooms fixtures & accessories repairing and replacements	FM Technicians	Outsourced Vendors
10	Construction works	• Gypsum board installations	Outsourced Vendors	FM Technicians
11	In-house installation works	• Refurbishment and renovations • work Stations setups • Lighting setups and installations • Electrical setups	FM Technicians	Outsourced Vendors

i	Scope	Description	Primary Task Owner	Secondary Task Owner
1 2	Finance works	• Receive vendor's invoices • Follow up with vendors to submit their invoices on time • Ensure all documents received • Ensure documents' validity • Initiate vendor's payments by raising PR tickets Raise a flag for delayed payments Share the POP with vendors	Senior Site Admin	FM Manager
1 3	Material selections and BOQs preparations	• Select the material required • Determine the specs and qty Ensures materials conform to Karm's standards	Supervisor	Manager
1 4	Planned preventive maintenance (PPM)	• Refer to the "Appendix" section	Supervisor	Manager
1 5	Periodic tests	• Maintains the system integrity and operation	Supervisor	Manager

i	Scope	Description	Primary Task Owner	Secondary Task Owner
1 6	Asset management	• Asset stock-take • Asset Tagging • Asset transportation • Asset book value • Asset depreciation	Supervisor & Technician	Manager
1 7	Scrap management	• Identify the scrap • Scrap approval • Scrap removal • Scrap's payment settlement	Senior Site Admin	FM Manager
1 8	Energy management	• Monitor and control energy usage • Integrate of renewable energy sources • Implement of smart grid technologies • Develop of energy conservation policies and regulations	Supervisor	Manager

- Scope: refers to the work type that FM Team covers.
- Description: refer to activities in detail within one scope.
- Primary Task Owner: refers to the main task owner within one scope.
- Secondary Task Owner: refers to the alternative task owner within one scope. Primary and secondary task owners can share the responsibility of one scope.

3.7 FM's KPIs

To evaluate the performance of FM Team, key performance indicators (KPIs) are set for different objectives. The below table display the FM's KPIs against set of Objectives:

Table 3 - FM's KPIs

i	Points	KPIs	Measuring Factor
1	Money savings and inhouse works	10%-20% cost reduction per year	Amount of money saved due to the inhouse works
2	Planned maintenance	80% compliance of the PPM	Completion percentage of the tasks of the PPM
3	Safety	Zero Incidents	Number of Incidents
4	Average time for completion	Average 30 days	Time taken to close tickets or projects including procurement/finance cycle
5	Projects	Above 90% Progress within the planned timeline	Projects Progress
6	Closing of FM Tickets	Above 90% of total FM Tickets	Closed FM Tickets against created and active tickets

3.8 FM's Delegation of Authority (DOA)

It is so important to delegate responsibilities among the team members. This allows for concentration of time on more important activities in the team. Further, it provides a sense of responsibility, a chance to grow, and exercise initiatives to whom the authority is delegated. In this section, The Responsibilities of FM Team are defined with a simple presentation for Authorities against each FM's Team members in the Delegation of Authority Matrix below:

Table 4 - FM's Delegation of Authority Matrix

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Policy - Creation/Editing					
Standard Operating Procedures - SOP		A	A	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
FM Regulati ons and Procedur es		A	A	A	A
Policy - Revision & Approval					
Standard Operatin g Procedur es - SOP		A	A	NA	NA
FM Regulati ons and Procedur es		A	A	NA	NA
Tickets Approvals					
FM Ticket		A	A	A	NA
PR Ticket		A	A	NA	NA
FIN Ticket		A	A	NA	NA
Proc Ticket (Jira)		A	A	NA	NA
Liquidati on Ticket		A	A	NA	NA
SLP Ticket		A	A	NA	NA
IT Ticket		A	A	NA	NA
HR Ticket		A	A	NA	NA

Process	Additional Notes	HOD	Manager	Supervisor	Senior Site Admin
Tickets Creation					
FM Ticket		A	A	A	NA
PR Ticket		A	A	A	A
FIN Ticket		A	A	NA	A
Scrap Ticket	Rev Ticket to receive payments from the vendor	A	A	A	A
FM Ticket Closing		A	A	A	NA
FM Ticket Changing Status		A	A	A	A
FM Ticket "Sent for Approval"		A	A	A	A
FM Ticket Cancellation, On-Hold & Rejection		A	A	A	A
Budget Determination	Alignment with the manager before sharing the budget	A	A	A	A
Budget Approval		A	A	NA	NA
Give Work Orders		A	A	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Set Priorities		A	A	A	A
Change in Work Sequence		A	A	NA	NA
Determine In-House Works		A	A	A	A
Communicate with Vendors	Initiation, Planning, Monitoring/Controlling and Closing	NA	A	A	A
Technical Discussion	stages	A	A	A	A
Lead the Site Survey		NA	A	A	NA
Give Technical Feedback	Alignment with the manager before sharing	NA	A	A	NA
Sign on Delivery Notes		NA	A	A	A
Take the Project Handover from the vendor	Supervisor or Manager should attend the handover	NA	A	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Sign on Handover Report	Team Leader or supervisor can sign on the Technical Report, but Manager must sign	NA	A	A	A
Share with the vendor the specs and BOQs	Alignment with the manager before sharing	NA	A	A	A
Receive Invoices	Hardcopy or Softcopy	NA	NA	A	A
Check that all documents received	Ex. Invoices, DNs, PO, E-Invoice, WHT if available	NA	A	A	A
Communicate with vendors for financial matters		NA	A	A	A
Sign on Delivery Notes		NA	A	A	A
Sign on Reports	Team Leader or supervisor can sign on the Technical Report, but Manager must sign	NA	A	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Accompany Vendor during the site Visits		NA	A	A	A
Supervise the vendor during the execution		NA	A	A	NA
Sign on HSE Permit to Work (PTW)	General, Isolation, Working at High, Hot Work, Electrical Work & Confined Space Permits	NA	A	A	NA
Manage HK People's Work	Give Orders, Distribute the manpower & Set Priorities	NA	A	A	A
Manage HK People' Attendance and Sign on Permissions	Annual Leaves, Sick Leaves & Leave Permissions	NA	A	A	A
Create Fingerprint Access		NA	A	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Add/Edit/ Delete in the HK Checklist s		NA	A	A	NA
Sign on the Daily Checklist s		NA	A	A	A
Give Permissi on for any requeste d external supports other than Houseke eping		NA	A	A	A
Commun icate with Pest Control Vendor	Arrange for Site Visits, Coordinate Technically with Vendor	NA	A	A	NA
Accompa ny the Pest Control Vendor during the site Visits		NA	NA	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Sign the Pest Control Checklist during the Pest Control Visits		NA	A	A	A
Sign on the Pest Control Technical Reports	Team Leader or supervisor can sign on the Technical Report, but manager must sign	NA	A	A	A
Approve on Annual Leaves		A	A	NA	NA
Approve on Leave Permissions and sign on it		A	A	NA	NA
Approve on Shifting the Week off		NA	A	A	A
Approve on OT	Unless Ops works overtime	A	A	NA	NA
Access to Main Electrical Room		NA	NA	A	A

Process	Additional Notes	HOD	Manager	Supervisor	Senior Site Admin
Define the Scraped Items	FM Ticket should be raised and then manager or Supervisor shall validate. HOD and Manager shall approve before the scrap vendor is communicated	NA	A	A	NA
Supervise the Scrap Removal		NA	A	A	A
Raise Rev Ticket		NA	A	NA	A
Receive the Scrap Weight Reports		NA	A	NA	A
Record in the Scrap Sheets		NA	A	NA	A
Share Scrap Report		NA	A	NA	A
Fill FM Team's Attendance Sheet		NA	A	A	A

Process	Additional Notes	H O D	Man ager	Super visor	Sen ior Site Ad min
Receive & Document the Daily Workload Records		NA	A	A	A
Receive & Document the Daily Checklists		NA	A	A	A
Document Vendors Invoices, DN, Reports & Technical Catalogues		NA	A	A	A

3.9 FM's Working Hours and Week-offs

In this section, FM Team's working hours and week-offs will be presented in the below table with number of Working Hours per week, Week-Off days, OT Eligibility, Shift-System Eligibility:

Table 5 - FM's Working Hours and Week-offs

i	Designation	Working Hours per Week (Hours)	Week-Off Days	Shift Timing (Morning/Night)	OT Eligibility (Yes/No)	Shift System Eligibility (Yes/No)
1	Manager	45	Friday - Saturday	Morning	No	No
2	Supervisor	45	Friday - Saturday	Morning	No	No
3	Senior site lead	45	Friday - Saturday	Morning	No	No
4	technician	45	Friday - Saturday	Variable	Yes	Yes
5	Admin Colleague	45	Friday - Saturday	Variable	Yes	Yes
6	Admin Colleague	45	Friday - Saturday	Variable	Yes	Yes
7	Admin Colleague	45	Friday - Saturday	Variable	Yes	Yes
8	Admin Colleague	45	Friday - Saturday	Variable	Yes	Yes

3.10 FM's Regulations and Policies

There are some rules and regulations which FM Team members follow to maintain a smooth and good quality of service:

- At least one representative from the FM Team shall be existing on site in each shift (Morning & Night Shifts).
- It is not necessary for FM Team to being presented with the vendors during the installation. Supervision from time to time is a must.
- It is necessary for FM Team to being presented with the vendors during any service & maintenance jobs (Ex: Pest Control, Regular Maintenances, Material Delivery, etc....)
- No vendor is allowed to start working on-site without HSE's permit to work.
- Annual leave & leave permissions shall be approved by the manager or HOD.
- If FM's member doesn't show up without prior notice, a penalty will be applied in coordination with HR Team.
- Any in-housework orders can be given by the supervisor in coordination with the manager.
- Technicians are not allowed to work in any job contrary to their technical backgrounds.
- If needed, HSE's permit to work shall be signed before any job order.
- It is not allowed to give vendors any of Karm's material even if it is a kind of help to accomplish his/her job without approval from the supervisor or the senior site lead.
- FM ticket should be raised before any job order to the FM's on-ground team.
Regular maintenance and emergency cases are not included.
- Technicians are not allowed to take job orders except from FM's supervisor, senior site lead or Manager.

4. FM's Standard Operating Procedure (SOP)

To maintain the same work pace for all FM Team members, Standard operating procedures aim to provide the policies, processes and standards needed for the organization to succeed. SOP can benefit the business by reducing errors, increasing efficiency and profitability, creating a safe work environment, and producing guidelines for how to resolve issues and overcome obstacles.

In this chapter, FM's SOP will be defined for each FM's scopes that are listed below. Each activity will be illustrated in detail with the guidelines for each scope. As mentioned previously, the ultimate goal of the FM Team is to make the core business and operation go smoothly and continuously.

To achieve the goal, FM Team carries out a group of responsibilities:

- Ticketing
- Project Management
- Scrap Management
- Soft Facility Management
- Asset Management
- Vendor Management
- Documentation

4.1 Ticketing

4.1.1 Facility Management Ticket (FM Ticket)

The “FM Ticket” is one of the tools that FM software offers to facilitate communication between the FM Team and other functions. FM Tickets are

normally raised by other functions requesting support from the FM Team.

FM Tickets could be for:

- Manpower supports
- Purchasing
- Technical supports
- Breakdown callouts
- Projects
- Soft facilities
- Asset transfers
- Refurbishments & renovations
- New site preparations
- In-house works
- Maintenance and repairing
- Emergency cases

4.1.2 Ticketing System

Ticketing System is a user-friendly online platform to ease communication between different teams across the organization. This allows teams to efficiently track tasks and issues throughout a project's lifecycle. Each ticket includes detailed information about the issue at hand, including priority level, status, and other relevant details. This makes it easy for team members to stay up to date on the status of each issue and collaborate effectively to find solutions.

4.1.3 FM Ticket Cycle and Process

FM Ticket passes through different stages. When FM Ticket is raised by a requester, it appears in the FM's dashboard with status of "Waiting for Support" with automatic reply is sent to the requester's email with this message *"Just confirming that we got your request. We're on it"*. FM Team then acts on it as follows:


- FM's manager or supervisor checks the FM Ticket on the same day of ticket creation date.

- FM's manager or supervisor checks the information in the FM Ticket and sets priority.
- If the ticket is with insufficient information or the business case is not provided, FM's manager or supervisor ask the requester to provide more information via a "Reply to Customer" comment.
- If there is no reply/feedback within **two working days** after FM's comment, FM Team has the right to close the ticket with this statement *"Since there is no resolution or feedback from the requester for more than **two working days**, kindly note that the ticket will be closed, Thanks"* with a resolution "Cancelled"
- FM's manager or supervisor studies the requirements and sets a budget and timeline (ETA) for execution process based on the classification of the FM Ticket.
- Execution timeline and ETA are determined based on o FM Ticket queue
 - o FM Ticket priority o FM Ticket classification (refer to FM Ticket Classification) o FM Ticket approvals date if needed
 - o FM Ticket pre-actions Ex. procurement process, material delivery, vendor on-site
- FM's manager or supervisor shares the budget if required as a comment to the requester and approvers.
- If needed, FM's manager or supervisor will send the ticket for approval based on the budget and business needs. (Refer to Approvers Matrix)
- If the FM Ticket is not approved by the approvers **within seven working days**, FM's manager or supervisor shall do a follow up with the approvers via email, teams or over a phone call.
- If the FM Ticket is not approved within **three working days** after the first follow up, FM manager or supervisor shall do one more follow up on the ticket and mention the approvers.

- If the FM Ticket is still not approved for more **two working days**, FM manager or supervisor has the right to close the ticket with this statement *"Ticket is not approved for more than **twelve working days**, kindly note that the ticket will be closed, Thanks"* with resolution "Rejected".
- If the FM Ticket requires external support from the procurement team, FM manager or supervisor (refer to DoA Matrix) shall raise procurement request Ticket with a detailed description and BOQ. Afterwards, PR number to be shared on the FM Ticket and change the status of the ticket to "Awaiting Procurement".
- After the FM Ticket is approved (if needed) or PO released and FM Team is ready to act upon the ticket or supervisor assign the ticket to the team leader or technician to start execution on ground based on the ETA shared on the ticket and FM Ticket's status shall be changed to "In Progress".
- After achieving the request of the FM Ticket, FM Team can close the FM Ticket with resolutions "Fixed" or "Done".

4.1.4 FM Ticket Flow Chart

Figure 1 - FM Ticket Process Flow Chart

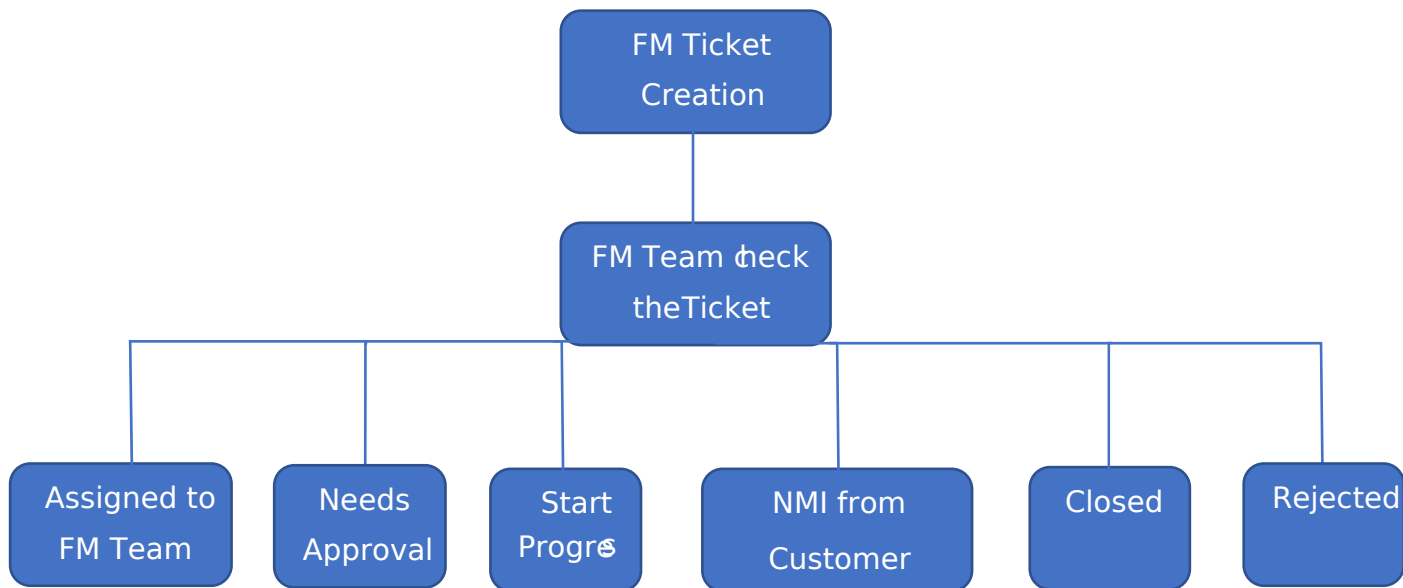

FM Ticket Process

- Any Task to be requested needs to go through raising FM Ticket.
- The first automatic status is “Ticket Waiting for Support”
- Ticket Assigned to FM Team/Rejected/Needs Approval/Start Progress

4.1.5 FM Ticket Status Definition

- **Ticket Assigned to FM Team:** the FM manager will assign the task to the available team based on the criteria of the job
- **Rejected:** the FM manager will reject the FM ticket if the scope is not clear even after customers' clarity is not valid.
- **Needs Approval:** the FM manager will request a cost/task approval from the requester's HOD.
- **Start Progress:** Once approval is granted, FM Team will start the work.
- **NMI From Customer:** If the request is not clear, FM Team will ask for more clarity.

- **Closed:** This is when the task is completed FM Team share pictures/comments and close the ticket

4.1.6 FM Ticket Policy

- FM's manager or supervisor has the right to close the FM Ticket without acting upon in the following case:
 - o Ticket Duplication (State the original FM Ticket number in the duplicated ticket) with resolution "Duplicated"
 - o Insufficient information provided and no reply with clear clarification from the requester. FM 's comment *"Since there is no resolution/feedback from the requester for more than **two working days**, kindly note that the ticket will be closed, Thanks"* with a resolution "Cancelled"
 - o Tickets are not approved, as per Approvers Matrix, for more than **twelve working days**, with a statement *"Ticket is not approved for more than **twelve working days**. Kindly note that the ticket will be closed, Thanks"* with a resolution "Rejected".
 - o If there is no business need from the request and this will be decided by the HOD. The FM Ticket will be closed directly with a statement *"Since there is no business need from your request according to the management team, kindly note that the ticket will be closed, Thanks"* with a resolution "Declined"
 - o FM Team has the right to put the FM Ticket "On-Hold" status if the top management decided to postpone the FM Ticket. If it exceeds **one Month** since changing the status of the FM Ticket to "On-Hold", FM Team has the right to close the FM Ticket with a statement *"Since no*

decision has been taken regarding this ticket, kindly note that the ticket will be closed, Thanks” with a resolution “Cancelled”

- FM Team shall update the status of the FM Ticket with each action on the ticket. Example: “Awaiting Procurement” or “Awaiting Approval”
- FM Team shall update the execution status of either progress or obstacle on the FM Ticket.
- FM Team shall respond for any comment on the FM Ticket within **two working days** max.
- For any inquiries to the requesters, it should be done either as a comment on the ticket, teams, or official email.
- ETA shared by the FM Team on the FM Ticket is for execution process only excluding the time taken for approvals and procurement process TAT.
- Budgets shared by FM Team on the FM Ticket are estimates and may vary according to the market status.
- Only FM’s HOD or manager has the right to edit on the FM Ticket’s details.
- FM Team shall act on FM Tickets except for emergency cases or direct instruction from FM’s HOD or manager.
- FM Team can raise FM Ticket in case that maintenance is required. FM Ticket shall be approved by the FM’s HOD before taking any action.

4.1.7 FM Ticket Assigning and Delegation

- FM manager or supervisor is authorized to assign the FM Ticket to themselves.
- FM’s manager or supervisor check if the FM Ticket is valid or not before assigning to other team colleagues.
- The assignment process should not take more than **two working days**.

- FM Ticket closing can be done by the manager or supervisor.

4.1.8 FM Ticket Approvers Matrix

Table 6 - FM Ticket Approvers Matrix

i	Purpose of FM Ticket	Size	Cost Range (EGP)		First Approver	Second Approver
			From	To		
1	Maintenance/Service	-	No Cost		Supervisor	FM Manager
2	Maintenance	Small	0	2,999	FM Manager	-
3	Maintenance	Medium	3,000	50,000	FM Manager	HOD
4	Maintenance	Big	50,000	Above	HOD	FM Manager
5	Service	Small	0	2,999	FM Manager	-
6	Service	Medium	3,000	50,000	FM Manager	HOD
7	Service	Big	50,000	Above	HOD	FM Manager
8	Material Purchasing	Small	0	2,999	FM Manager	-
9	Material Purchasing	Medium	3,000	50,000	FM Manager	HOD
10	Material Purchasing	Big	50,000	Above	HOD	FM Manager
11	Hiring Manpower	-	0	Above	HOD	-
12	Leasing Service	Small	0	2,999	FM Manager	-
13	Leasing Service	Medium	3,000	50,000	FM Manager	HOD
14	Leasing Service	Big	50,000	Above	HOD	FM Manager
15	Refurbishments & Renovations	-	1000	Above	FM Manager	HOD
16	Relocations	-	1000	Above	FM Manager	HOD
17	Projects	-	1000	Above	FM Manager	HOD

4.1.9 FM Ticket Classification

Table 7 - FM Ticket Classification

i	FM Ticket Type	Nature of FM Service	FM Category	Priority
1	Type I	Regular Maintenance	Man Hours	Low
2	Type II	Breakdown	Man Hours	High
3	Type III	Manpower Service (Soft Facilities)	Man Hours	Medium
4	Type IV	Manpower Headcount	Service / Vendors	Low
5	Type V	Service	Service / Vendors	Medium
6	Type VI	In-Housework	Material & Man Hours	Medium
7	Type VII	Installations	Service / Vendors	Medium or High
8	Type VIII	Material Purchasing	Material	Medium
9	Type IX	Equipment Leasing Request	Service / Vendors	Medium
10	Type X	Emergency	Man Hours & Service / Vendors	High

4.1.10 FM Ticket Communication Matrix

Table 8 - FM Ticket Communication Matrix

i	FM Ticket Type	Nature of FM Service	FM Category	1st Communicator		2nd Communicator		3rd Communicator		4th Communicator	
				Type	Mean of Communication	Type	Mean of Communication	Type	Mean of Communication	Type	Mean of Communication
1	Type I	Regular Maintenance	Man Hours	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Procurement	PR Ticket and/or Email	Safety Team	Email, Work Permit, or meeting

i	FM Ticket	Nature of FM Service	FM Category	1st Communicator		2nd Communicator		3rd Communicator		4th Communicator	
	Type II	Breakdown	Man Hours	Procurement	PR Ticket and/or Email	Vendor	Email or Phone Call	Requester	FM Ticket Comment or Email	-	-
2	Type II	Breakdown	Man Hours	Procurement	PR Ticket and/or Email	Vendor	Email or Phone Call	Requester	FM Ticket Comment or Email	-	-
3	Type III	Manpower Service (Soft Facilities)	Man Hours	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Procurement	PR Ticket and/or Email	-	-
4	Type IV	Manpower Headcount	Service / Vendors	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Procurement	PR Ticket and/or Email	-	-
5	Type V	Service	Service / Vendors	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Procurement	PR Ticket and/or Email	Safety Team	Email, Work Permit, or meeting
6	Type VI	In-House work	Material & Man Hours	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Safety Team	Email, Work Permit, or meeting	-	-
7	Type VII	Installations	Service / Vendors	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Procurement	PR Ticket and/or Email	Safety Team	Email, Work Permit, or meeting

i	FM Ticket	Nature of FM	FM Category	1st Communicator		2nd Communicator		3rd Communicator		4th Communicator	
	Type	Service Material			FM Ticket Comment or Email		FM Ticket or Email		PR Ticket and/or Email		
8	Type VIII	Material Purchasing	Material	Requester		Approver		Procurement		-	-
9	Type IX	Equipment Leasing Request	Service / Vendors	Requester	FM Ticket Comment or Email	Approver	FM Ticket or Email	Procurement	PR Ticket and/or Email	Safety Team	Email, Work Permit, or meeting
10	Type X	Emergency	Man Hours & Service / Vendors	Notified Person	Phone Call	Safety Team	Phone Call	Top Management	Phone Call	HR Team	Phone Call

4.1.11 FM Ticket Timeline

In this section, the average Turnaround Time (TAT) is illustrated for each type of FM Tickets as per “FM Ticket Classification”. The average TAT is summation of the average time taken in each step:

- Creation: Average time taken to check the FM Ticket and classify the type.
- Study: Average time taken to study the requirements and if there is inquiry from the requester
- Approval Cycle: Average time taken to get the approval on the FM Ticket
- Procurement Process: Average time taken starting from raising PR till releasing the PO

- Execution (ETA): Average time taken to execute the work whether this work will be done in-house or by vendor

Table 9 - FM Ticket Timeline

i	FM Ticket Type	Nature of FM Service	Average Timeline (Working Days)					
			Creation	Study	Approval Cycle	Procurement Process	Execution (ETA)	TAT
1	Type I	Regular Maintenance	1	2	8	15	3	29
2	Type II	Breakdown	1	0	0	0	1	2
3	Type III	Manpower Service (Soft Facilities)	1	2	8	15	1	27
4	Type IV	Manpower Headcount	1	2	8	15	3	29
5	Type V	Service	1	2	8	15	3	29
6	Type VI	In-Housework	1	3	8	15	4	30
8	Type VIII	Material Purchasing	1	3	8	15	3	30
9	Type IX	Equipment Leasing Request	1	2	8	15	3	29
10	Type X	Emergency	1	0	0	0	0	1

Notes:

- Timeline cycles can vary depending on the response of the other stakeholders.
- Time dedicated for each process is an average.

- Procurement Process Timeline is as follows; PR creation, approval cycle, RFQ stage & PO release. The process time can vary based on the cost and size of the work.
- Execution (ETA) for “In-House works & Installations” is based on the size of the installations.
- Execution (ETA) for “Soft Facilities & Manpower Headcounts” is based on the average time taken for vendors to respond. This time could vary if the vendors responded late.
- The above table “FM Ticket Timeline” is to give a quick perception to the requester about the time taken to make his/her request done.

4.1.12 FM Ticket Criteria

In this section, the FM Ticket’s criteria will be listed to ensure the validity of the request and to FM Team to act upon.

- FM Ticket shall be raised by Karm’s employee only.
- FM Ticket shall be raised by Team Leader’s or above
- FM Ticket shall be with clear title, description, location, category, priority/severity, department & defined requester. If this information is not clear, FM Team has the right to close the ticket.
- Requester shall justify the ask by attaching a business case in the FM Ticket in the following cases:
 - o **New Assets:** When requesting new assets for your department or facility.
 - o **New Project:** When initiating a new project that requires FM support.
 - o **New Setup (Infrastructure):** When setting up a new facility or office space.
- The FM Ticket’s status shall be changed according to its status.

- FM HOD or manager are authorized to do edits on the FM Ticket details.
 - Requester/reporter shall attach a business case if the request is one of the following:
 - o New Assets
 - o New Project
 - o New Setup
- Any different cases, requester/reporter is not required to attach a business case

4.1.13 Procurement Tickets (PR Tickets)

Sometimes, FM Team need an external support from Procurement Team to:

- Purchase material
- Call vendors for installation works
- Create AMCs
- Release POs regards the manpower/visits like HK, helpers & pest control
- Renew the contracts
- Equipment or Space Lease

For this reason, there must be guidelines to regulate the process of PR Tickets:

- FM Team shall create PR Tickets based on APPROVED FM Tickets as a reference. If there is no reference for the PROC Ticket, Approval shall be obtained in written from FM's HOD and to be attached in the PR Ticket.
- FM Team shall attach cost/manpower breakdown, detailed BOQs with a clear description for each item, layouts, estimated budget and clear scope of work.
- For the requests that are related to a signed contract, the PO request can be raised without raising a PROC Ticket.

- In case it is a repeated request, FM Team raises a PR Ticket for a procurement confirmation without sharing further SSF.
- In some cases, FM Team can share already existing offers in the PROC Ticket as a kind of support to the procurement team.
- FM Team shares technical feedback only.
- FM Team shall invite potential vendors for a site survey, if needed, before sharing any feedback with the Procurement Team. (Refer to “Site Surveys” section)
- FM Team shall conduct technical meetings to discuss the technical matters in coordination with the Procurement Team.
- The same information shall be delivered to all potential vendors to avoid any misleading or manipulation.
- FM Team shall respond to Procurement’s inquiries or calls for feedback within **two working days**
- Vendor management scope for the FM Team is in the execution and payments stages only.
- According to the DOA, FM’s manager, supervisor & senior site admin are authorized to raise PR Tickets.

Site Survey:

- If a site survey is required, it should be mentioned in the PR Ticket.
- Site surveys shall be done before any technical feedback shared to the Procurement Team
- The same person shall do the site surveys with potential vendors for one job.
- FM Team shall share the status and outcomes of the site surveys by email with the Procurement Team.

4.1.14 PO Tool Requests

- In case it is decided not to go with an L1 vendor, FM Team shall obtain exceptional approval and to be attached within the PR request.
- In case it is repeated request, FM Team can take confirmation from procurement to go with the previous SSF as long as the prices as the same. Procurement confirmation shall be attached to the PR request.
- For the requests that are related to a signed contract, PO requests can be raised without raising a PR Ticket or procurement confirmation. Only the cost breakdown shall be attached to the payment request.
- In urgent case, FM Team can obtain an exceptional approval from the HOD to proceed immediately without PO release, while the PO is raised and in the approval cycle
- Urgent cases are defined by FM manager and to be communicated by FM manager to the top management/HOD for exceptional approval.

4.1.15 Finance Tickets (Payment Requests)

Part of the vendor management cycle is the closing process. FM Team is responsible for initiating the payment process after the service is delivered by the vendor. The service could be:

- Material purchases
- Installations
- Maintenance
- Facility leasing
- MHE and equipment renting
- Soft facilities
- Manpower (helpers)

FM Team raises FIN Tickets to initiate the payment process cycle after receiving the documents required. Thus, there must be guidelines to regulate the process of FIN Tickets:

- According to the DOA, FIN Tickets can be raised by FM's manager or admin senior colleague.
- FM Team shall do follow up with vendors regarding the invoices after the service in the PO is provided.
- The FM Team shall ensure that all required documents are received.
 - 1- E-Invoice
 - 2- Normal Invoice with a signed declaration for E-invoice non-registration
 - 3- WHT if required (Applicable for Egypt only)
 - 4- Delivery notes if required
 - 5- Completion reports if required
 - 6- Service report if required
 - 7- Approved PO
 - 8- Signed contract if required
 - 9- Commercial register if required
- FM Team shall raise the FIN Ticket after receiving all required documents by **one working day** max.
- In case of advance payment, FM Team shall attach the approved PO
- According to the DOA, service reports shall be signed by FM's manager or supervisor. In case the team leader signed, Manager's signature must be existed.
- According to the DOA, completion reports shall be signed by the manager or supervisor. In case the team leader signed, Manager's signature must be existed. According to the DOA, delivery notes can be signed either by FM's manager, supervisor, or team leader.
- FM's admin colleague is not authorized to sign any of the above listed documents by any means.

- FM Team shall share the proof of payment (POP) with vendors after their payments are processed if requested.
- FM Team shall respond on the finance team inquires within **one working day**; otherwise, it may take more than one day if vendors do not respond on FM's communication shortly.
-

4.2 Project Management

In this chapter, one of the main FM's scopes will be explained in detail. Again, FM Team acts as the executing arm for the organization. Of course, the success of any corporate is measured by complying with the organization's goals and projects in terms of quality, time, and cost. FM Team contributes to achieving organization's goals by managing their projects and making it real.

FM Team take care of three broad categories of projects: Strategic Projects, Operational Projects, and Compliance Projects:

- **Strategic Projects** involve creating something new and innovative. A new facility and site preparation might be a strategic project because it will allow an organization to gain strategic advantage over its competitors.
- **Operational Projects** improve current operations. These projects may not produce radical improvements, but they will reduce costs, get work done more efficiently, or facilitate operational activities.
- **Compliance Projects** must be done to comply with an industry or governmental regulation or standard. Often there is no choice about whether to implement a project to meet a regulation, but there may be several project options to consider, any of which would result in meeting compliance requirements.

4.2.1 Projects Scope of Work

FM Team is responsible for any project related to the:

- Infrastructure setups
- Constructions
- Site preparations
- New system installations
- New equipment installations

Excluding:

- O&M main grids
- IT projects (Network Infrastructure, Access Points & Access Readers)

4.2.2 Projects Classification

i	Project Category	Project Size	Project		Average Project Timeline
1	Operational Projects	Small	Reallocations		1-2 Months
			Maintenance & Repairing		
	Strategic Projects	Medium	Setups and Constructions		3-2 Months
			System Implementation		
			System Improvement		
	Compliance Projects	Big	Site Preparation		6-3Months
			Infrastructure Setup		
			Site Evacuation		

Table 10 - Projects Classification

4.2.3 Project Management Process

FM Team follow the five phases of the project management to ensure that the project's deliverables and goals. The five phases are:

Figure 2 - Project Management Process (PMI)

5 Basic Phases of Project Management



a. Project Initiation

In this stage, FM Team receives the request or the idea from the requester and turns it into a meaningful goal. In most cases, the request

comes in an official email or FM Ticket. The requester usually is either function's HOD or Top Management for big projects.

- Internal meetings are conducted among the FM Team and start open discussions.

FM Team then figure out the following:

- Estimated costs
 - Tentative timelines
 - List of activities
 - Expected deliverables
 - Project scope
 - Project constraints
 - Identifying the stakeholders
- After completing this task, FM Team shall conduct a kick-off meeting with all internal stakeholders to share the information gathered for the project.

Approvals then to be taken from the top board.

b. Project Planning

After the project is approved by top management, FM Team starts studying the project in detail.

- FM Team lays out the project's roadmap as the following:
 - o Prepare detailed description for each scope of work
 - o Prepare BOQs and layouts
 - o Prepare breakdown for activities if possible

FM Team then starts to raise PR tickets by attaching the above documents.

- After the RFQ is initiated by the Procurement Team, FM Team starts to conduct technical discussions and invite vendors for site surveys. Multiple RFQs can be initiated for each scope of work.
- After potential vendors submit their offers. FM Team shall study the technical offers and then give technical feedback for each offer submitted.
- Weekly calls shall be made between all stakeholders for updates and inputs.

c. Project Execution

After POs released, FM Team starts the execution phase of the project taking into consideration operational seasons:

- A kick-off meeting to be conducted with all stakeholders internally. This step shall be done for each scope of work.
- A preparation meeting shall be conducted with the vendor to discuss the timelines, working hours, HSE rules, and regulations. This meeting must be attended by FM HOD or FM manager, FM Team, HSE Team, and any other functions related to the project.
- FM Team shall prepare an 'Action Log' for each scope and to be shared with all stakeholders.
- Weekly meetings shall be conducted to share the progress/blockers of the project.
- FM Team shall supervise the vendor on site and monitor the progress.
- FM Team shall facilitate the site for vendors
- FM Team is the point of contact between vendors and other functions. Actions to be communicated with FM Team first. FM Team then will deliver the communicated actions to the vendors.

The HSE Team shall ensure that vendors are ready to work as per their rules and regulations.

- Vendors shall sign "Permit to Work" before starting to work on ground. This must be done daily.

- For material delivery, DNs to be signed by FM Team as per the DOA.

d. Project Monitoring and Controlling

During the execution phase, FM Team shall monitor the progress and work compliance.

- FM Team shall update the “Action Log” with the status and progress.
- FM Team shall ensure that project is on track and on time as per the ETAs.
- The FM Team shall share the progress sheet with all stakeholders.

e. Project Completion

In this final phase of project management process, FM Team is responsible for closing the project internally and with vendors.

- FM Team shall set a date for project handover from the vendor. The requester shall attend this session and share his comments in an official email along with other stakeholders. Handover communication shall be addressed to all stakeholders.
- FM Team prepare a snag list including other functions comment and to be addressed in official email to the vendor
- Project can be handed over on phases and same steps shall be followed in each phase.
- Completion report shall be signed by the vendor, FM representatives, HSE Team and other related stakeholders. The selection report shall include the snag list.

FM Team shall raise FIN Tickets for vendor’s payments after completion of report signed.

- The above steps can be done in phases based on the milestones & PO payment terms.

4.2.4 New Facility Scouting & Preparations

In case Karm added a new facility to be under its operations, there are some steps shall be followed:

- Obtain a clear plan and clear requirements and dates including the scope and purpose of the opening (recommended 1 year period (deadline) buffering).
- Scouting of the facilities including (facility assessment by FM team - the quality of the facility - assessment if the facility meets the requirements obtained from the requester- FM team shares technical assessment for the proposed facility), if the scouting resulted into the accepted facility by the FM Team, they would go to the further process actions.
- FM Team communicates with procurement and legal to check the legal aspects with the landlord including (Civil Defense - facility license - other legal documents)
- If legally approved, FM team will start to communicate with others to submit their assessment and feedback.
- If all functions confirmed, procurement start to contact the landlord regarding the commercial and contractual matters along with the FM team.
- Procurement team share the results of the negotiations with landlord and the contract to the top management.
- IF top management approved, procurement along with the FM team will start the contract process.

After the contract is signed, each function will start to prepare or raise their PR Tickets to the procurement team.

4.2.5 Closing & Evacuating Facility

In case Karm management decided to close one of its facilities, there are some steps shall be followed:

- In case of any near expiry of the rent contract, the FM will raise the flag to obtain approval for renewal or discontinuing 3 months before expiry.

- If discontinuing, the operation shall provide an evacuation plan with a Deadline based on the size of the facility; also, the destination must be provided.
- After operation evacuation, FM Team shall make a stock take for all assets.
- After stock take, FM starts planning for resources needed for evacuation and issue the Procurement Tickets.
- Execution of the evacuation plan based on the assigned plan and PO.
- After finishing the evaluation, the Procurement, FM Team and legal team do a handover to the landlord with consideration of the contract terms and insurance paid.

Facility Closure Checklist

1. **Receive FM Ticket**

- **Step 1:** Receive the Facility Management (FM) ticket to initiate the closure process.

2. **Coordinate with Operations**

- **Step 2:** Work with the Operations (OPs) team to set a due date for clearing out from the facility.

3. **List and Prepare Assets**

- **Step 3:** Create a list of all FM and Karm assets to prepare for the movement.

4. **Conduct Stock Take**

- **Step 4:** Perform a stock take to inventory all assets.

5. **Procure Dismantling Services**

- **Step 5:** Collaborate with the Procurement team to identify vendors for dismantling Karm assets if needed.

6. **Arrange Transportation**

- **Step 6:** Coordinate with the procurement team to arrange trucks for transferring assets.

7. Transfer Assets

- **Step 7:** Initiate the transfer process after receiving confirmation from a kick-off meeting involving Heads of Departments (HODs).

8. Terminate Services

- **Step 8:** Communicate with the Procurement team to terminate contracts with housekeeping and pest control vendors.

9. Site Survey

- **Step 9:** Contact the Landlord (LL) to conduct a site survey and review any snag list if it exists.

10. Return Facility Keys

- **Step 10:** After clearing the facility of all Karm assets, return the facility keys to the LL.

11. Complete Handover Reports

- **Step 11:** Sign both copies of the handover reports between Karm and the LL.

12. Request Security Deposit

- **Step 12:** Send an email to the LL, including the Finance team, to request the return of the security deposit if applicable.

4.3 Scrap Management

In this section, the scrap process will be described extensively. There are scraps and wastes that come out due to the operations.

4.3.1 Scrap Definition

Scrap is the leftover items/pieces that are unrepairable and not needed anymore by the cooperate. Usually, FM Team decides that this scrap cannot be maintained, and no benefits cannot be taken out of it. There are three types of scrap material:

- Operation Disposal
- General scrap
- Environmentally harmful scrap

4.3.2 Operation Disposal

Operation Disposal refers to the waste generated from operational activities. The disposal process is a routine task, occurring multiple times per request (refer to section 4.3.6 for Scrap Collection Frequency). This type of scrap/recycling does not require prior approval to proceed. Our typical disposals include:

- Cartons
- Stretch

4.3.3 General Scrap

This kind of scrap is defined as non-harmful scrap and can be disposed of by any vendor. Our scrap is normally

- Wood like white wood & red wood
- Metals like steel, iron, Aluminum, etc.
- Plastics
- Damaged Assets, Equipment, Device, Machine, Tool, or Component

4.3.4 Environmentally Harmful Scrap

This kind of scrap is defined as environmentally harmful disposals and can be disposed of by specific vendors who have Sanitary landfills approved by the government. Environmentally harmful scrap:

- Oil
- Lubricant
- Batteries
- Biological items
- Cartridge toners
- Acid water

4.3.5 Disposal Process and Policy

The process for getting rid of the disposal should be clearly defined to prevent conflicts and ensure transparency:

- **Disposal Material:** Only cartons and stretch films are to be disposed of. Any other materials will be classified as scrap and will require a different disposal process.
- **Weight Scale Report:** The vendor must provide a weight scale report for each visit. This report can be either consolidated for all sites or separate for each site.
- **Report Collection:** The FM Team is responsible for collecting the scale reports from the vendor and following up on any delays.
- **Weight** validation should be performed on-site if a Pascol Scale (Truck Scale) is available. Alternatively, A Karm representative should accompany the vendor to the nearest authorized scale to verify the weights.
- **Disposal Breakdown:** The FM Team must create a breakdown report detailing visit dates, corresponding weights, and disposed materials.

- **FIN Tickets:** The FM Team is responsible for raising FIN Tickets to the Finance Team, including all required documents: Signed Contract, Disposal Breakdown, and Scale Receipts. FIN Tickets are submitted once the scrap is collected.
- **Document Validation:** The Finance Team is responsible for validating the submitted documents to ensure that rates and quantities match the contract. If discrepancies are found, the Finance Team will flag the ticket for the FM Team to correct and resubmit.
- **E-Invoice Sharing:** Once the Finance Team issues the E-Invoice, the FM Team must forward it to the vendor for payment.
- **Payment Deadline:** The vendor has a 15-day grace period from the E-Invoice issuance date to make the payment. The FM Team must obtain proof of payment (either a transfer or deposit confirmation).
- **Proof of Payment:** The FM Team should attach the proof of payment to the corresponding FIN Ticket.
- **Non-Payment Follow-Up:** If the vendor does not pay within the grace period, the FM Team will send an official communication (with Procurement and Finance Teams copied). Continued non-payment will lead to escalation to the Procurement Team for a replacement and to the Legal Team for potential legal action.
- **Account Validation:** The Finance Team is responsible for confirming that the payment has been reflected in Karm's account and must raise an immediate flag if the payment does not appear.
- **Bank Account Details:** The Finance Team must provide bank account details to all stakeholders to prevent incorrect or rejected transfers/deposits.

Payment Terms: Payment terms may vary according to the contract.

Payment Exceptions: In cases of delays in contract signature or E-

- Invoice issuance, a consolidated payment plan will be proposed for Management and Finance Team approval and alignment.
- **Rate Commitment:** Both the FM Team and the Finance Team are committed to adhering to the rates specified in the contract.

4.3.6 Scrap Process and Policy

Disposing of the scrap shall follow a clear process to avoid any conflicts and lack of transparency:

- Scrap refers to any damaged asset, equipment, device, machine, tool, or component that is beyond repair and cannot be reused.
- The FM Team is responsible for initiating a scrapping proposal via email to the Management, Finance, SLP, Site Lead, and HSE Team, including all relevant details about the assets in question.
- If the proposal originates from a stakeholder other than the FM Team, the stakeholder must submit an FM Ticket.
- An inspection committee, consisting of representatives from Finance, SLP, FM, HSE, and the Site Lead, will review the proposed items.
- All committee members must sign a confirmation form certifying that the items are eligible for scrapping.
- The FM Team will raise an SLP Ticket for the proposed items to obtain approval.
- After weighing the items and obtaining the scale receipt, the FM Team is responsible for raising a REV Ticket. This ticket should include the committee confirmation, Signed Contract, Disposal Breakdown, and Scale Receipts.

The Finance Team is responsible for validating the submitted documents to ensure that rates and quantities match the contract. If discrepancies are

- found, the Finance Team will flag the ticket for the FM Team to correct and resubmit.
- Once the Finance Team issues the E-Invoice, the FM Team must forward it to the vendor for payment.
- The vendor has a 15-day grace period from the E-Invoice issuance date to make the payment. The FM Team must obtain proof of payment (either a transfer or deposit confirmation).
- The FM Team should attach the proof of payment to the corresponding REV Ticket.
- If the vendor does not pay within the grace period, the FM Team will send an official communication (with Procurement and Finance Teams copied). Continued non-payment will lead to escalation to the Procurement Team for a replacement and to the Legal Team for potential legal action.
- The Finance Team is responsible for confirming that the payment has been reflected in Karm's account and must raise an immediate flag if the payment does not appear.
- The Finance Team must provide bank account details to all stakeholders to prevent incorrect or rejected transfers/deposits.

4.3.7 Scrap Collection Frequency

Scrap vendor collects the scrap from all sites per request.

4.4 Soft Facility Management (SFM)

Soft Facility Management is part of FM Team's scope. Soft facilities are the services that the business relies on to maintain a pleasant, healthy, and safe working environment. In Karm, SFM covers two main services:

- Housekeeping Services (HK Services)
- Pest Control Services

4.4.1 Housekeeping Services (HK Services)

• Housekeeping Scope

- o Cleaning, dusting, vacuuming, and disinfecting floors, walls, and ceilings.
- o Removal of waste and any other garbage
- o Cleaning of baskets, wastepaper baskets, etc. and disposing off all the collected refuse at designated sites daily.
- o Spraying Room Fresheners in all rooms, daily at regular intervals.
- o Cleaning and disinfecting all fixtures including toilet bowls, urinals, sinks, toilet seats, etc. Brush thoroughly to include below water level and under rims including areas at hinges and cistern handles. Restock toiletries which include liquid hand soap, air fresheners, naphthalene balls in toilets etc., after daily check-ups in the morning, afternoons and on call basis during daytime.
- o Cleaning and dusting of light fixtures, fans, air conditioner vents, overhead light fixtures, projectors, fire-fighting equipment, nameplates, plant boxes, door mats, etc.
- o Placing garbage bags, scrub stretching, scrub cartoons etc. in all garbage bins to avoid stains and stinks and clear them on a daily basis.
- o Materials handling and carrying upon request from Facility Team Only.

Sweeping, cleaning, mopping, and polishing with disinfectant/cleaner of the area covered under the contract, including (reception, Stairs, offices, meeting rooms, corridors, Masjed, locker rooms, lockers, toilets, and cafeterias etc.).

المكاتب وأماكن العمل

م	البند / المهمة	التكرار	التوقيت
1	تفريغ سلال المهملات وتغيير الأكياس	يومي	صباحاً ومساءً
2	مسح المكاتب والأسطح بمواد مطهرة	يومي	صباحاً
3	تنظيف الشاشات ولوحات المفاتيح	يومي	صباحاً
4	كنس/مسح الأرضيات	يومي	صباحاً
5	تنظيف النوافذ والواجهات الزجاجية الداخلية	أسبوعي	بداية الأسبوع
6	تلميع الأثاث الخشبي والمعدني	أسبوعي	بداية الأسبوع
7	تنظيف عميق للسجاد (غسيل)	شهري	نهاية الشهر

منطقة الاستقبال

م	البند / المهمة	التكرار	التوقيت
1	تنظيف مكتب الاستقبال	يومي	صباحاً
2	مسح وتلميع الأرضيات	يومي	صباحاً

م	البند / المهمة	التكرار	التوقيت
3	تنظيف الزجاج والأبواب الأمامية	يومي	صباحاً
4	تنظيف مقاعد وأثاث منطقة الانتظار	يومي	صباحاً
5	إزالة الغبار عن اللوحات والديكورات الجدارية	يومي	صباحاً
6	تعطير المكان والتحقق من عدم وجود روائح	يومي/ عند الحاجة	صباحاً

المطبخ

م	البند / المهمة	التكرار	التوقيت
1	غسل الأواني والأكواب	بعد كل استخدام	على مدار اليوم
2	تنظيف وتعقيم أسطح العمل والطاولات	عد كل استخدام	على مدار اليوم
3	تنظيف الأحواض	على مدار اليوم	صباحاً
4	تنظيف الثلاجة من الداخل والخارج	أسبوعي	بداية الأسبوع
5	تنظيف الميكروويف وماكينة القهوة/الغلاية	يومي	على مدار اليوم
6	تفريغ سلة المهملات	يومي	على مدار اليوم
7	مسح الأرضيات وتجفيفها	يومي	على مدار اليوم
8	تنظيف عميق للخزائن والأدراج	أسبوعي	بداية الأسبوع

دورات المياه

م	البند / المهمة	التكرار	التوقيت
1	تنظيف وتعقيم المراحيض	يومي	صباحاً
2	تعبئة الصابون والمناديل والمطهرات	يومي / عند الحاجة	على مدار اليوم
3	مسح الأرضيات وتجفيفها	يومي	على مدار اليوم
4	تنظيف المرايا والحوامل المعدنية	يومي	صباحاً
5	تفريغ سلات المهملات	يومي	على مدار اليوم
6	التحقق من عمل المعطرات الآلية وتعبئتها	يومي	صباحاً
7	تنظيف عميق للبلاط والجدران	أسبوعي	بداية الأسبوع

الممرات والمناطق المشتركة

م	البند / المهمة	التكرار	التوقيت
1	كنس ومسح الأرضيات	يومي	على مدار اليوم
2	تنظيف الحوائط	أسبوعي	بداية الأسبوع
3	تفريغ سلات المهملات	يومي / عند الحاجة	على مدار اليوم
4	إزالة الغبار عن لوحات الإرشاد والمخارج	يومي	على مدار اليوم

قاعات الاجتماعات

م	البند / المهمة	التكرار	التوقيت
1	تنظيف الطاولات والكراسي	بعد كل اجتماع	صباحاً
2	ترتيب الكراسي وإعادة تجهيز القاعة	بعد كل استخدام	صباحاً
3	كنس/مسح الأرضيات	يومي	صباحاً
4	تفريغ سلة المهملات	يومي	صباحاً ومساءً

• **Housekeeping Headcount and Manpower Distribution**

Table 11 - Housekeeping Headcount and Manpower Distribution

Location	Staff	Working Days
Karm Solar	<u>6</u> Housekeeping staff - Morning Shift - 12 working hours + 1 Supervisor	6 Days

• **Housekeeping SOP**

o HK Team is FM Team's responsibility which means FM Team who gives orders and instructions.

- o HK attendance is taken daily according to the manpower plan shared with the vendor.
- o HK daily attendance is taken manually and biometrically.
 - o HK checklist shall be filled daily by the HK Team.
- o HK vendor is paid on the attended headcount only unless the contract is SLA Contract.
- o HK performance is evaluated by FM Team.
- o Penalty Matrix applied as follows:

م	المخالفة	المرّة ١	المرّة الثانية لنفس الشهر	المرّة الثالثة لنفس الشهر	المرّة الرابعة لنفس الشهر	المرّة الخامسة لنفس الشهر	المرّة السادسة لنفس الشهر	ملاحظات
١	الأداء – ملاحظات متكررة وثغرات في جميع المواقع والأنشطة	ارسال ايميل	عقد اجتماع	750	1000	1000	1000	تُضاف 1000 جنيه لكل غرامة لاحقة
٢	نقص في المواد	ارسال ايميل	عقد اجتماع	250	500	1000	1000	تُضاف 1000 جنيه لكل غرامة لاحقة
٣	نقص الحضور	يُطبّق الخصم عن كل وردية غياب وفقاً للحضور						—
٤	عدم ارتداء الزي	إنهاء خدمة العامل	إنهاء خدمة العامل	إنهاء خدمة العامل	إنهاء خدمة العامل	إنهاء خدمة العامل	إنهاء خدمة العامل	—
٥	التقاعس والتدخين	100 جنيه	200 جنيه	300 جنيه	إنهاء خدمة العامل	إنهاء خدمة العامل	إنهاء خدمة العامل	—
٦	مخالفات السلامة	100 جنيه	200 جنيه	300 جنيه	إنهاء خدمة العامل	إنهاء خدمة العامل	إنهاء خدمة العامل	—
٧	مخالفات السرقة/التلف	بناءً على قيمة العناصر التالفة/المفقودة						يُصدّر إشعار مدين بقيمة العناصر التالفة/المفقودة، وذلك بعد اثبات الواقعة و باتفاق الطرفين.

4.4.2 Pest Control Services

Pest Control is part of the FM Team's responsibilities. FM Team supervises the process of controlling, managing, minimizing, and removing undesirable insects and other pests, for Karm's facilities.

• Pest Control Scope

Table 12 - Pest Control Scope

i	Scope
1	Pest Control Service shall cover all types of reptiles like rats, rodents, mice, snakes, geckos, worms, etc.
2	Pest Control Service shall cover all types of insects like flies, ferrets, bees, ants, cockroaches, flying cockroach beetles, Scorpions, etc.
3	Pest Control Service shall cover all types of birds like small birds, pigeons, crows, etc.
4	Pest Control Service shall cover all types of vermin like algae, mold, worms, etc.
5	Pest Control Service shall cover all types of animals like cats, dogs, kitties, etc.

• Pest Control SOP

- o Safety must approve the MSDS used material before use it
- o One of the FM representatives should accompany the PC site team during his weekly visit and fill out the checklist. (Refer to Checklists Templates)
 - o Checklists should be reviewed and signed by the compliance Team.
- o For the trapped pests, FM Team shall communicate with the vendor to remove it to avoid any decomposition and biological & hygienic hazards.

- o In case that vendor is not committed to the agreed visits per month, FM Team shall escalate to Procurement Team for every incident.
- o FM Team is responsible for checking the status of PC regularly through weekly checkups in the Facilities.
- o FM Team should abide by PC instructions and recommendations.
- o PC Vendor shall submit reports for each visit and to be signed by either FM's supervisor or Manager as per the DOA.
- o FM Team should consider the quality of service provided in the payments and apply penalties as per Penalty Matrix.
- o Evaluation of PC service will be decided by Karm's compliance Team & FM Team.
- o Any losses or damages due to poor PC service, Ops Team will decide the value of the loss to be deducted from the monthly invoices as per Penalty Matrix.
- o PC service shall cover:
 - Outside the Premises
 - Indoor (Warehouse & Admin Building)
 - Utility Rooms
- o Every trap or device related to the pest control must be in a drawing layout and must have an identification and check list attached.
- o No of Visits to be decided by the vendor according to the status of the facility and his experience.
- o Any dead animal to be disposed of within 24 hours.

• **Pest Control Penalty Matrix**

Table 13 - Pest Control Penalty Matrix

Violation	Penalty for 1st time	Penalty for 2nd time	Penalty for 3rd time	Penalty for 4th time	Penalty for 5th time	Penalty for 6th time
Lack of Commitment on the Agreed Plan. عدم الالتزام بالأعمال المتفق عليها وفقا لخطة التشغيل او عدم تنفيذ اي من البنود المتفق عليها	Official Warning Communication	Official Warning Communication	0.2X Deduction	0.5X Deduction	0.75X Deduction	Termination

Violation	Penalty for 1st time	Penalty for 2nd time	Penalty for 3rd time	Penalty for 4th time	Penalty for 5th time	Penalty for 6th time
Poor Pest Control Quality. It will be decided by Karm's Compliance Team جودة خدمة المكافحة سيئة. فريق الجودة الخاص ينون سوف يحدد مستوى الخدمة بعد تقديم تقرير مفصل بالقصور بالخدمة ان وجدت	Official Warning Communication	Official Warning Communication	0.2X Deduction	0.5X Deduction	0.75X Deduction	Termination
Not showing up on the agreed 'visits Dates عدم الحضور في الزيارات المنفق عليها	Official Warning Communication	Official Warning Communication	0.5X Deduction	0.75X Deduction	Termination	

Violation	Penalty for 1st time	Penalty for 2nd time	Penalty for 3rd time	Penalty for 4th time	Penalty for 5th time	Penalty for 6th time
Using unauthorized materials استخدام مواد غير متفق عليها	Official Warning Communication	Official Warning Communication	Termination			
Losses due to poor quality حدوث خسائر بسبب سوء الجودة	Official Warning Communication	Losses will be deducted from the vendor. Ops will determine the cost of damaged items	Losses will be deducted from the vendor. Ops will determine the cost of damaged items	Losses will be deducted from the vendor. Ops will determine the cost of damaged items	Termination	
Violation	Penalty for 1st time	Penalty for 2nd time	Penalty for 3rd time	Penalty for 4th time	Penalty for 5th time	Penalty for 6th time

Violation	Penalty for 1st time	Penalty for 2nd time	Penalty for 3rd time	Penalty for 4th time	Penalty for 5th time	Penalty for 6th time
Not responding to emergency visits عدم الاستجابة للزيارات الطارئة	Official Warning Communication	Official Warning Communication	Losses will be deducted from the vendor. Ops will determine the cost of damaged items	Losses will be deducted from the vendor. Ops will determine the cost of damaged items	Termination	
X	Refers to the Monthly Invoice					

4.5 Vendor Management

Vendor Management is an important part of FM's scope of work. The FM Team coordinates and cooperates with third-party (product or service) providers. This happens through different activities that are done by FM Team:

- Facilitate and maintain relationships between your organization and vendors/partners
- Prepare the site for vendors.

- Ensure a smooth execution process by coordinating with other stakeholders and eliminating any internal blockers.
- Analyze quality metrics and KPIs.
- Enforce vendors to follow the safety regulations and processes.
- Communicate with vendors in pre-execution stage for the technical matters.
- Take a proper handover from vendors and apply the “Project Completion” process.
- Ensure that all documents are received and documented (Ex. Warranty, Catalogues, Handover Reports, etc.)

4.5.1 Vendor List and Classification

There are different classifications for the vendors that serve Karm’s facilities; MEP, Hydraulics, MHE, Generator, Pest Control, HK, Racking and Shelving, Automated Conveyors, Elevators, General Fit-Outs, Scrap Collection, Asset Transportation & Security Systems. The table below illustrates the vendor list and their classifications:

Table 14 - Vendor List and Classification

i	Service	Service Type (Maintenance, Service, Leasing, Material Supply, or Installation)	Activities	Vendors
3	MHE	Leasing	Leasing of Electrical RT, Electrical Hand Jacks & Diesel Forklifts	3R
				Unimar
				Santrac
		Maintenance	Regular Maintenance	Finet
				Unimar
				EgyBrit

i	Service	Service Type (Maintenance, Service, Leasing, Material Supply, or Installation)	Activities	Vendors
			for Electrical RT, Electrical Hand Jacks & Diesel Forklifts	3R
4	Generator	Maintenance	Regular Maintenance for the Generator	Masters Al Mostaqbel El Shorouk
		Leasing	Leasing of Generators	Comax
5	Pest Control	Service	Provide Pest Control	Trully Nollen
				TRUE
				Toxido
				SWF
				Technical Group
				Orkin
6	HK	Service	Provide Housekeeping	City Services
				Sun Service
				G4S
				CBRE
				System One
				Plus Ways
				AGES
				Protection
				Trust Egypt
				Regency
7	Racking and Shelving	Installation	Pallet Racks and Picktower Installations	Toxido
				Purelife
				Kemt
				Technometal
				Linkmisr

i	Service	Service Type (Maintenance, Service, Leasing, Material Supply, or Installation)	Activities	Vendors
				Beeco
8	Automated Conveyor	Installation	Automated Conveyor Installations	EgyRoll
				EFE
				LogSquare
		Maintenance	Automated Conveyor Maintenance	LogSquare
9	Elevator	Maintenance	Elevator Maintenance	EgyBrit
				LogSquare
		Installation	Elevator Installation	EgyBrit
				LogSquare
10	General Fit-Outs	Material Supply	Supplies and General Contracting	Al Mostaqbel
				El Shorouk
				ABM
				BM 360
				Masters
				Al Fotouh
				Archi Touch
				Bavaria
				Benchmark for Supplies and Contracting
				Capital Office Furniture
				Catering Plus
				El Helow Furniture
				Future Builders
				Go-Up
				Hitron for Construction & Supplies
				MESC

i	Service	Service Type (Maintenance, Service, Leasing, Material Supply, or Installation)	Activities	Vendors
				Nepton for General Contracting
				Nile Engineering Services
				Al-Masrya for Supplies & Contracting
				Finet
				Spectrum For General Supplies
i	Service	Service Type (Maintenance, Service, Leasing, Material Supply, or Installation)	Activities	Vendors
				National Eng. Supply Co.
				Delta
		General Services	Ex. Gas/Diesel Refuel	Total
		General Maintenance	Electrical, Plumbing & Small Constructions	Industria Limited Egypt
11	Scrap Collection	Service	Collect the Scrap	WMC
12	Asset Transportatio n	Service	Providing Trucks and Trellas	U Drive
13	Security Systems	Installation	Install Security Systems	Nepton for General Contracting

i	Service	Service Type (Maintenance, Service, Leasing, Material Supply, or Installation)	Activities	Vendors
				Al-Masrya for Supplies & Contracting
				Crystal
				Masters
				Plugs
		Maintenance	Maintain Security Systems	Nepton for General Contracting
				Al-Masrya for Supplies & Contracting
				Crystal
				Masters
				Plugs

4.5.2 Vendor Management Process and Policy

- FM Team is designated only for the technical aspects and forbidden to communicate with vendors for any commercial matters.
- FM Team can assist the Procurement Team in the “Vendor Sourcing” process.
- FM Team can act immediately and call the vendor on site in case of emergencies without going through the normal procurement cycle. This should be approved by FM’s HOD first.
- FM Team can ask for quotations from vendor in alignment with Procurement Team. Quotations shall be attached to the PR Tickets.
- Site surveys and technical discussions shall be conducted by FM Team before sharing the technical feedback to Procurement Team.

- In case of site surveys needed for validation, FM Team shall state this in the PR Ticket.
- It is forbidden that FM Team shares any submitted quotations with vendors.
- FM Team is the POC along with Procurement Team regarding vendors.
- FM Team is responsible for creating entry permits for vendors.
- FM Team should ensure that vendors have all required PPEs and follow HSE standards.
- FM Team is responsible for initiating the vendors' payments after receiving the service.
- For Projects, FM Team shall conduct a kick-off meeting with all stakeholders including vendors before proceeding with any job on ground.
- FM Team shall evaluate the vendor's performance for each service provided. Also, the overall vendor performance shall be shared with the Procurement Team.

4.5.3 In-House Scope VS Outsource Scope

There are two ways to accomplish the duties and tasks either to be done by insourced technicians (In-House) or seek intervention from experienced outsourced vendors (Outsource). This is decided upon the case where:

Selecting In-House Option Criteria:

- **Technical Knowledge:** Our insourced technicians have the technical knowledge of the required task.
- **Warranty:** The Warranty of the device, equipment, or the system is expired, and FM Team is allowed to interfere.
- **FM's Schedule:** There are free timeslots in the FM's schedule to perform the task according to its timeline.

- **Project Scale (Small & Medium):** Normally, FM Team takes over small and medium projects due to limitation of tools and resources.
- **Complexity:** Insourced technicians usually execute repeated and generic works. Some Projects/tasks require special skills and knowledge
- **Criticality & Urgency:** In some cases, the task is critical and urgent, which is forced to intervene by the insourced technicians. Most important is to align with the management to accept possible risks.

Selecting Outsource Vendor Option Criteria:

- **Technical Knowledge:** If the project/task requires special and unique of skills and knowledge
- **Warranty:** The Warranty of the device, equipment, or the system is still valid. The manufacturer/supplier is responsible for maintaining if the warranty is valid.
- **FM's Schedule:** FM's Schedule is too tight and will take time to be done in-house.
- **Project Scale (Big):** Big and complicated projects usually are assigned to external professional vendors.
- **Complexity:** Some Projects/tasks require special tools and resources which is not available for FM Team.
- **Criticality & Urgency:** In some cases, we go with outsourced vendors as it will be faster and more efficient.
- **Contractual:** In case there is a signed and valid contract.

In-House Scope

- Regular Maintenance & Breakdowns:
FM Team is responsible for fulfilling the requesters' request and responding to any breakdowns.
- Carpentry & Blacksmith Works:

This is limited to wooden pallets repair, trollies/Benz welding & fixation or any small fabrications that might help in the installations.

Electrical Installation Works:

FM Team is responsible for installing/modifying/repairing any electrical setup.

- Plumbing Installation Works:

FM Team is responsible for installing/modifying/repair in the plumbing/FF network.

- CCTV Installation Works:

FM Team is responsible to install/modify/repair the CCTV as the following:

- Infrastructure Setup
- Cameras Installation
- View Angle Adjustment
- System Maintenance
- CCTV Maintenance

- Material Inventory

FM Team is responsible for managing the stock of the spare parts and monitoring the consumption and ordering rates. The below screenshot is an example for our stock management

Figure 3 - Screenshot for FM Stock Sheet

1	A	B	C	D	E	F	G	H	I	J	K
	Item		Material	Unit	Category	Net Qty (Formula)	Consumed	Ordered	Safety Stock	Surplus or Deficit (Formula)	Order Qty (X2) (Formula)
2	1		tie wrap pack 50 cm	Pack	General	18	13	31	20	-2	22
3	2		tie wrap pack 70 cm	Pack	General	30	13	43	20	10	0
4	3		external electrical socket	Each	Electrical	184	80	264	50	134	0
5	4		female electrical socket	Each	Electrical	19	5	24	10	9	0
6	5		c-clamp 2 cm	Each	General	280	150	430	100	180	0
7	6		c-clamp 3 cm	Each	General	150	108	258	100	50	0
8	7		junction box 10*15	Each	General	10	79	89	100	-90	190
9	8		panel 4-ways	Each	General	9	12	21	20	-11	31
10	9		galvanised flexible roll 20 mm	Roll	Electrical	65	14	79	10	55	0
11	10		plastic flexible roll 25 mm	Roll	Electrical	0	3	3	10	-10	20
12	11		plastic flexible roll 20 mm	Roll	Electrical	1	4	5	10	-9	19
13	12		iron flexible roll 30 mm	Roll	Electrical	5	0	5	10	-5	15
14	13		iron flexible roll 20 mm	Roll	Electrical	1	0	1	10	-9	19
15	14		مسامير بوزة 2 سم ,nail	Pack	General	8	1	9	30	-22	52
16	15		مسامير بوزة 3 سم ,nail	Pack	General	10	0	10	30	-20	50
17	16		مسامير بوزة 4 سم ,nail	Pack	General	15	0	15	30	-15	45
18	17		مسامير بوزة 8 سم ,nail	Pack	General	14	1	15	30	-16	46
19	18		مسامير سلف 2 سم رأس مفك ,nail	Pack	General	99	2	101	30	69	0
20	19		iron rod 10 mm, ثيش	Each	General	80	0	80	50	30	0
21	20		electric key 40A	Each	Electrical	2	10	12	10	-8	18
22	21		electric key 32A	Each	Electrical	20	9	29	10	10	0
23	22		electric key 20A	Each	Electrical	33	10	43	10	23	0
24	23		electric key 25A	Each	Electrical	4	3	7	10	-6	16
25	24		electric key 16A	Each	Electrical	83	25	108	10	73	0
26	25		binary electric key 32A	Each	Electrical	1	0	1	5	-4	9
27	26		binary electric key 63A	Each	Electrical	1	0	1	5	-4	9
28	27		contactor 50A	Each	Electrical	1	0	1	5	-4	9

Figure 3 - Screenshot for FM Stock Sheet

Outsource Scope

- Special Installations/Services:
Projects with special installations are assigned to outsource for their knowledge. For the services, HK, Pest Control, Consultancy, Designing is assigned to outsource vendors
- Racking and Shelving Installations
Since racking and shelving requires a high level of skills and is very special, it is assigned to outsource vendors.
- MHE Maintenance
For the rented MHEs, Part of the contract is that vendors are responsible for maintaining their machines regularly.
- Constructions:
Constructions always need special tools/resources; that's why it is assigned to outsource vendors.
- Material Supplies:
Vendors are assigned to buy the required materials from the market against released PO.

4.5.4 Vendors Key Performance Indicators (Vendors' KPIs)

In this section, certain criteria will be listed to evaluate the performance of vendors. There are two types of criteria in which whether the vendor comes through a contract providing services every periodically or one-type-job vendor through a PO.

• Contractual Vendors

As mentioned before, Contractual Vendors are vendors who provide services periodically or every certain period. That type of vendor has different criteria since the nature of service, scope, timeline, and handover are different. For this reason, the following criteria are to evaluate the vendors of this type, and

their final score is shared with procurement team to update the vendor list according to the vendors' evaluation:

Table 15 - Contractual Vendor Evaluation Criteria

N O	Services	KPI REPORT	Severi ty	Comme nt
1	Schedule of Planned Preventive Maintenance (PPM)	Establish a Schedule of PPM with details and number of resources allocated, consumables, equipment & tools for every PPM	Medium	Minimum KPI 2.5/5
2	Report of each PPM performed inclusive of details of Consumable and Spare Parts	Establish a detailed service activity report for each PPM/Work order performed per Asset, , inclusive of Consumables and Spare Parts which are required for the Employer to purchase in case of Replacement during the visit. The Service Provider is required to obtain the signature from the Employer's Utilities Manager On its report after each PPM is performed for each Asset.	Medium	Minimum KPI 2.5/5
3	Expert/ Supervisor Inspection Reports	A Monthly inspection by the Expert FM/HSE Supervisor to evaluate the levels and effectiveness of PPM provided by the Service Provider for each Asset. The recommendations/ points of improvements to the PPM and overall condition of each Asset in visit reports.	High	Minimum KPI 2.5/5

N O	Services	KPI REPORT	Severity	Comment
4	Services Call Logs & Actions taken by the Service Provider	All Services calls recorded and attended by Service Provider with time of call (max 4hrs), time of attendance, time of Service and details of service call witnessed and signed by the Employer's representative. in case of any malfunction should also be described including remedy measures taken to avoid such malfunctions in future. Recorded material / Asset's misuse, waste & damaged	High	Minimum KPI 3.5/5
5	Absenteeism	Staff availability per Shift to be recorded in biometric, no absenteeism allowed, provide replacement for sick leaves	Medium	Minimum KPI 2/5
6	Timely Service	Planned Schedule of each PPM Service vs actual Service	Medium	Minimum KPI 2.5/5
7	Competency of Staff	Provision of competent and trained staff who understand the industry norms, professional in their fields, follow hygiene best practice and adhere to the Employer's requirements	High	Minimum KPI 3.5/5
8	HSE	Provision to adhere to personal and overall cleanliness in execution of Services. Proper PPE and Uniform and adhere to overall HSE requirements	High	Minimum KPI 3.5/5
9	Quality of Services Executed	Records of reactive services performed and fixed right first time without repeated failures of the same nature	High	Minimum KPI 3.5/5
10	Availability of Materials used for Services (Consumables) & Spare Parts	Recommended spare parts to be provided by the contractor and available a site as per the AMC	High	Minimum KPI 3.5/5

N O	Services	KPI REPORT	Severi ty	Comme nt
11	Response Time	Records of Responses at all Service Calls and Fixing of issue times max 4hr as per AMC	High	Minimum KPI 3.5/5
12	Reporting & KPIs	Quality and Timely submission of Reports and contractors' KPI availability for Monthly meeting reviews	High	Minimum KPI 3.5/5
13	System availability	To ensure system available 98%	High	Minimum KPI 3.5/5
14	Shutdown time	To adhere to Karm PTW Shutdown and minimize the Shutdown time & breakdown	High	Minimum KPI 3.5/5

Table 16 - Vendors Rating Scale

Score	Legend	Penalty
Below 40	1. Poor	10% Deduction from the Contract Value
Below 45	2. Under performance	5% Deduction from the Contract Value
45	3. Acceptable	
46-50	4. Good	
51-70	5. Excellent	

• One-Type-Job Vendors

One-Type-Job Vendor are the vendors who perform one job once against released PO. Those vendors have different criteria for evaluation. Also, their final scorecard is calculated by taking the average score of their total jobs assigned to them.

To improve the vendor management process, KPIs should be set to evaluate the performance and value of the service provided by the vendors. There are six standards that FM Team should rely on while evaluating any job done by vendors which are:

- Response Time
- Adherence and Compliance to the Requirements

- Service Timeline
- Quality of Service
- Service Delivery and Handover
- Warranty

Table 17 - Vendors' KPIs

i	KPI	Description	Severity
1	Response Time	Response Time KPI is to measure the amount of time it takes for vendors to Respond to our calls after receiving the PO. This metric is important because it can help FM Team determine how efficient vendors are. Vendors are evaluated on each service provided and evaluated according to the Rating Scale.	High
2	Adherence and Compliance to the Requirements	Adherence and Compliance KPI is to measure the commitment of vendors to the requirements and scope of work. This allows FM Team to have deeper insights into vendors' performance and help to evaluate vendors in terms of strengths and weaknesses. Also, it shows to what extend vendors follow the rules and regulations of HSE and FM.	High
3	Timeline	Timeline KPI is to measure the time taken by vendors to accomplish the job. This helps to track whether the project/service provided on time and if it's not, tracking where it's off- The target is important so FM Team can always have an estimated completion date in upcoming jobs.	Medium

i	KPI	Description	Severity
4	Quality	Quality KPI is to measure the quality of service provided by vendors. Also, this helps to evaluate the vendors in terms of quality of work and whether the product/service is sustainable, safe, reliable, and friendly environmental or not.	High
5	Delivery & Handover	Delivery & Handover KPI is to measure the efficiency of the handover process and delivery of service. This helps to ensure that all required documents are submitted or not like handover reports, Catalogues, Manuals, etc.	Medium
6	Warranty	Warranty KPI is to decide whether vendors offer warranty or not	Medium

• Vendors Rating Scale

FM Team is evaluating the vendors based on the above KPIs using the below metric. FM Team give a score from 1 to 5 for each KPI as per the below table. Rating is done for each service provided by vendors. At the end of each time cycle, average score is calculated for each KPI for all vendors to obtain an overall rating for vendors' performance. Scores are recorded in the "Vendor Evaluation" Register. This should be shared with Procurement to eliminate the low-performance and inadequate vendors.

Table 18 - Vendors Rating Scale

Score	Legend	Penalty
Below 40	1. Poor	10% Deduction from the Contract Value
Below 45	2. Under performance	5% Deduction from the Contract Value
45	3. Acceptable	
46-50	4. Good	
51-70	5. Excellent	

4.6 Asset Management

Asset Management is part of FM's scope in terms of recording, maintaining, purchasing, and scrapping the assets that are owned by the business. Asset Management is an important scope, first, to make it easy for the business to keep track of assets, whether liquid or fixed. Second, keep tracing the periodic maintenance for each asset to increase the durability and save the book value of the assets for a longer time.

4.6.1 Asset Register

FM Team records each and every asset owned by Karm. Assets are classified according to Asset Description, Asset Type, Country, Location, Asset Category. These data are provided by the FM Team. On the other hand, the Finance Team is responsible for recording the PO Number, Purchasing Price, Net Book Value, Depreciation, Scrapped, or not.

FM Team counts all the assets and created a register for all assets across all facilities. The asset tag has been created and attached to each asset.

4.6.2 Asset Tagging

Asset Tag consists of three parts: Country Code, Asset Category Code, and Tag Serial Number: 01-102-1000001



• Asset Tagging Guidance

Table 19 - Asset Tagging Guidance - Country Code

Country Codes	
Code	Country
01	EGY

Table 20 - Asset Tagging Guidance - Asset Category

Asset Category Codes	
Code	Asset Category
101	Computer & IT Equipment
102	Furniture & Fixtures
103	Vehicles
104	Facility & Logistics Equip
105	Office Equipment

Table 21 - Asset Tagging Guidance - Fixed Assets

Fixed Assets Tagging Guidelines					
Asset Type	Tagging Required?	IT/Non-IT	Dept's	Asset Category Code	Asset Category Description
Air Conditioners	Yes	Non-IT	FM	105	Office Equipment
Bar Code / PDA Scanners	Yes	IT	IT	104	WH & Logistics Equip
Biometric Machines	Yes	Non-IT	FM	105	Office Equipment
Building	No	Non-IT	FM		
Bullet & Dome Camera	Yes	Non-IT	SLP	101	Computer & IT Equipment
Cabinets & Shelves	Yes	Non-IT	FM	102	Furniture & Fixtures
Cash and documents safe	Yes	Non-IT	FM	105	Office Equipment
CCTV DVR	Yes	Non-IT	SLP	101	Computer & IT Equipment

Fixed Assets Tagging Guidelines					
CCTV Monitors	Yes	Non - IT	SLP	101	Computer & IT Equipment
CCTV-Back Box Camera Bracket	No	Non - IT	SLP	101	Computer & IT Equipment
Chair	Yes	Non - IT	FM	102	Furniture & Fixtures
Civil Works/Electrical Works/Cabling/Fabrication/Ducting Work/Painting work/Sprinkler	No	Non - IT	FM		
Cleaning Equipment	Yes	Non - IT	FM	105	Office Equipment
Conveyor Belt	Yes	Non - IT	FM	104	WH & Logistics Equip
Data Center cooling Unit	Yes	IT	IT	101	Computer & IT Equipment
vans	Yes	Non - IT	FM	103	Vehicles
Desert Coolers	Yes	Non - IT	FM	105	Office Equipment
Desktops	Yes	IT	IT	101	Computer & IT Equipment
Drawer units	Yes	Non - IT	FM	102	Furniture & Fixtures
Employee lockers	Yes	Non - IT	FM	102	Furniture & Fixtures
Face Detection Attendance	Yes	Non - IT	SLP	105	Office Equipment
Fans	Yes	Non - IT	FM	105	Office Equipment

Fixed Assets Tagging Guidelines					
Finger Print & Card Reader	Yes	Non - IT	SLP	105	Office Equipment
Finger Print Machine	Yes	Non - IT	SLP	105	Office Equipment
Firefighting Equipment	Yes	Non - IT	FM	105	Office Equipment
Forklift	Yes	Non - IT	FM	104	WH & Logistics Equip
Freezers and Chillers	Yes	Non - IT	FM	104	WH & Logistics Equip
Frisking Kiosk	Yes	Non - IT	SLP	105	Office Equipment
Headphones/Headsets	No	IT	IT	101	Computer & IT Equipment
ladders	Yes	Non - IT	FM	104	WH & Logistics Equip
Landline Telephone	Yes	IT	IT	105	Office Equipment
Laptops	Yes	IT	IT	101	Computer & IT Equipment
Metal gate detectors	Yes	Non - IT	SLP	105	Office Equipment
Microwave	Yes	Non - IT	FM	105	Office Equipment
Mobile Phones	Yes	IT	IT	101	Computer & IT Equipment
Multi Door Locker	Yes	Non - IT	SLP	104	WH & Logistics Equip

Fixed Assets Tagging Guidelines					
Network Video Recorder	Yes	Non - IT	SLP	101	Computer & IT Equipment
Lockers	Yes	Non - IT	FM	104	WH & Logistics Equip
Pallet Truck	Yes	Non - IT	FM	104	WH & Logistics Equip
Paper Shredder Machine	Yes	Non - IT	FM	105	Office Equipmen t
Locker	Yes	Non - IT	FM	104	WH & Logistics Equip
Trolley	Yes	Non - IT	FM	104	WH & Logistics Equip
Plastic Totes	No	Non - IT	Warehou se & Logistics	104	WH & Logistics Equip
Port Separate Switches	No	Non - IT	FM		
Port Switches entire Unit	Yes	Non - IT	FM	105	Office Equipmen t
Power HVAC Unit	Yes	Non - IT	FM	105	Office Equipmen t
Power Supply Unit	Yes	Non - IT	FM	105	Office Equipmen t
Printers	Yes	IT	IT	101	Computer & IT Equipment
Screen	Yes	IT	IT	101	Computer & IT Equipment
Projector	Yes	IT	IT	101	Computer & IT Equipment

Fixed Assets Tagging Guidelines					
Racking system	No	Non - IT	FM	104	WH & Logistics Equip
Refrigerator	Yes	Non - IT	FM	105	Office Equipmen t
Safe Locker	Yes	Non - IT	FM	102	Furniture & Fixtures
Scrubbing Machine	Yes	Non - IT	FM	104	WH & Logistics Equip
Servers	Yes	IT	IT	101	Computer & IT Equipment
Shrink Wrap Machine	Yes	Non - IT	FM	104	WH & Logistics Equip
Small Battery Cells	No	Non - IT	IT		
Sofa	Yes	Non - IT	FM	102	Furniture & Fixtures
Software	No	IT	IT	101	Computer & IT Equipment
Sort Working Station	Yes	Non - IT	FM	104	WH & Logistics Equip
Sorter	Yes	Non - IT	FM	104	WH & Logistics Equip
Sound System	Yes	IT	IT	105	Office Equipment
Table	Yes	Non - IT	FM	102	Furniture & Fixtures
Television	Yes	IT	IT	105	Office Equipment
Thermal camera	Yes	Non - IT	SLP	105	Office Equipment

Fixed Assets Tagging Guidelines					
Trollies	Yes	Non - IT	FM	104	WH & Logistics Equip
UPS	Yes	IT	IT	105	Office Equipment
UPS Battery/Big Batteries	Yes	IT	IT	105	Office Equipment
Vehicles & Delivery Trucks	Yes	Non - IT	FM	103	Vehicles
Video Conferencing	Yes	IT	IT	101	Computer & IT Equipment
Water Dispenser	Yes	Non - IT	FM	105	Office Equipment
Wooden Pallet	No	Non - IT	Warehouse & Logistics	104	WH & Logistics Equip
Workstations	Yes	Non - IT	FM	102	Furniture & Fixtures
Reach Truck	Yes	Non - IT	FM	103	Vehicles

4.6.3 Asset Transfers

- FM Team take care of any asset transfer.
- Any asset transfer shall be done through FM Team.
- FM Team is responsible for the transfer process including asset preparation and wrapping, truck requests, loading, and offloading process.
- Requestor shall raise FM Ticket or send an email to FM Team to do the transfer.
- All asset transfer requests shall be approved by the FM's HOD or manager.
- FM Team should update the asset register for every transfer that happened.

- The FM Team shall have a transfer tracker.

4.6.4 Asset Stock-Take

- FM Team shall do a stock-take for all assets across all fulfilment centers every 3 months.

4.6.5 Asset Management Policy

- FM Team shall create asset tags for all assets according to Asset Tagging Guidance
- FM Team shall have a register with the following data for already-existed assets, new assets and transferred assets: PO Number, Description, Asset Category, Asset Location & Asset Tag Number.
- FM is responsible for any purchasing, transferring, and scrapping any assets that belong to any facility.
- FM Team should update the asset register for every purchase, transferring, and scrapping happen.
- All asset transfer requests shall be approved by the FM's HOD or manager.
- The FM Team shall have a transfer tracker.

4.7 Documentation

4.7.1 FM Leaves and Attendance

Everyone in the Facility team has the right to take vacations for any reason. We will now list the vacations for everyone and please adhere to the number of vacations and follow the required procedures:

• Type of Leaves

Table 22 - Type of Leaves

Type of leave	Number of Days
Annual leave	21 (7 casual days, maximum 2 consecutive casual days)
Hajj Leave	
Cultural Leave	
Marriage Leave	
Paternal leave	
Paid Sick Leave	

• Leaves Policy

Annual Leave (15 days)

- Inform the direct manager about the date and duration.
- Make sure that there is enough balance from the HR team.
- Sending mail to be approved by the FM manager prior to the annual leave.

Casual Leave (6 casual days with a maximum of 2 consecutive casual days)

- Inform the direct manager by phone.
- Make sure that there is enough balance from HR team

Marriage Leave (3)

- Inform the direct manager about the date and duration.
- Make sure that there is enough balance from the HR team.

- Sending mail to be approved by the FM manager prior to the annual leave.

Paternity Leave (1)

- Inform the direct manager about the date and duration.
- Make sure that there is enough balance from the HR team.
- Sending mail to be approved by the FM manager prior to the annual leave.

Sick Leave (30 days)

- Inform the supervisor or TL about the date and duration.
- Make sure that there is enough balance from the HR team.
- Sending mail to be approved by the FM manager prior to the annual leave.

Permits Policy

Staff will be allowed to request permission to leave early but the following steps must be followed:

- Inform the supervisor or the TL about the reason and must be approved by the FM manager.
-

Shift Change Policy

Employees will be allowed to request a shift change from morning to evening or vice versa, but the following steps must be followed:

- Inform the supervisor or the TL about the reason and must be approved by the FM manager.

Changing of the Week-off Policy

Employees will be allowed to request a change of week-offs (temporarily or permanently), but the following steps must be followed:

- Inform the supervisor or the TL for the reason and to be approved by the FM manager.

Note: Changing the leave does not consider working overtime

- **Overtime (OT) System**

Overtime Types

- i. Extra hours for 9 working hours
- ii. Work 6-7 days a week (will be determined by the HR team)
- iii. Work on official occasions and holidays (will be determined by the HR team)
- iv. In case of emergency after the completion of the official shift

Overtime Policy

- FM manager and HOD approval are required over a mail sent prior to the overtime required.

• Deduction Policy

- Late working hours (official timings from 8 am to 6 pm)
- Absence without reason, notification, or filling the permit
- Inaction or non-compliance

Note: Whoever does not follow the instructions will be sent to HR for investigation.

4.7.2 Daily Report

Daily Reports are done by each technician daily to list the activities that happened throughout the day. The aim of such reports is to keep track of the technicians' activities and to analyze their productivity. Submitted reports are revised by FM's supervisor and manager to check the productivity.

Daily Reports are recorded in a sheet to be as a database for any future purposes.

4.7.3 Checklists

There are different types of checklists that have been filled out by FM Team to track the status of Karm's assets and enable FM Team to be proactive and avoid breakdowns. Here is the Checklist Schedule:

Table 23 - Checklist Schedule

i	Checklist	Description	Frequency	Note
1	FM Daily Report	Actions done throughout the day	Daily	Filled by FM Team
2	Utility Checklist	Electricity Readings, Water Readings,	Daily	Filled by FM Team
3	Housekeeping Checklist	Areas that have been cleaned by HK Team to track their performance	Daily	Filled by FM Team
4	Stock Consumption Checklist	Monitoring the stock consumption on daily basis	Daily	Filled by FM Team

4.7.4 Attendance

FM Team attendance is mandatory for the payroll and tracking of the leaves taken by each member of FM Team. Monthly Attendance Report is submitted by HR Team for validation. Attendance is recorded by the Biometric Method.

• Biometric Method

Each member in the FM Team obligated to do fingerprints daily to validate his presence. New joiners must be registered in the biometric system from day one.

Note: Please refer to “FM’s Working Hours and Week-offs” to know the working hours and week-offs for each FM member.

5. Catering Services Procedure

5.1 Routine / Day-to-Day Catering

1. Site Facility Coordinator (or FM & Admin at HQ) maintains a standing weekly/monthly catering schedule with the approved vendor(s) for routine pantry or refreshment service.
2. Any change to standing quantities, or schedule is submitted by the Requester (or department representative) at least 2 working days in advance.
3. Site Facility Coordinator confirms the change with the vendor and updates the site log.

5.2 Event / Meeting Catering Requests

4. Requester submits a catering request (via the FM request form/email/ticketing tool in use) stating event date and time, location/site, headcount, meal type or menu preference, and cost center/budget code.
5. Requests should be submitted at least 3 working days before the event; urgent requests (under 24 hours) are handled per Section 9 (Exceptions).
6. Site Facility Coordinator or FM & Admin obtains a quotation from an approved vendor and confirms availability.
7. Request is routed for approval per the Approval Matrix in Section 7.
8. On approval, the order is confirmed with the vendor in writing (email or vendor portal), specifying delivery time, quantity, and cost.
9. Site Facility Coordinator inspects the delivered order for quantity, quality, and hygiene before service, and logs to any discrepancy.

5.3 Vendor Management

- Only vendors on the FM & Admin Approved Vendor List may be used for business catering.
- New vendors are vetted by FM & HSE for food safety/hygiene certification, pricing, and reliability before being added to the list.
- Vendor performance (timeliness, quality, complaints) is reviewed periodically; underperforming vendors are flagged for review or removal.

5.4 Quality, Hygiene & Food Safety

- Site Facility Coordinator checks that delivered food is at the correct temperature, properly packaged, and within any stated shelf life.
- Any hygiene or quality concern is documented with photos where possible and reported to FM & Admin on the same day.
- Recurring issues with a vendor triggers a formal vendor review per Section 5.3.

5.5 Invoicing, Payment & Reconciliation

10. Vendor submits invoice referencing the confirmed order/PR number.
11. Site Facility Coordinator or FM & Admin verifies the invoice against the delivered order and approved quotation.
12. FM & Admin consolidates verified invoices monthly per vendor and site, and forwards to Finance/Admin for payment with supporting documentation.
13. Finance/Admin processes payment per the standard vendor payment cycle and confirms FM & Admin.

5.6 Records & Documentation

- FM & Admin maintains a catering log (per site) capturing date, requester, event/purpose, headcount, vendor, cost, and approval reference.

6. Courier Services Procedure

6.1 Request Initiation

14. Requester submits a courier request stating pickup and destination address, item description, urgency/required delivery time.
15. For sensitive or high-value items, the Requester flags this explicitly so FM & Admin can act accordingly.

6.2 Approval & Spend Thresholds

16. Routine, low-cost courier requests within the standing budget are approved directly by the Site Facility Coordinator or FM & Admin.
17. Requests above the standard cost threshold, or involving international/express service, are routed per the Approval Matrix in Section 7.

6.3 Dispatch

18. FM & Admin/Site Facility Coordinator selects one of our couriers based on urgency, destination, and item type.
19. Dispatch is booked and confirmed with sender and receiver
20. The item is handed over against a signed pickup log if required.

6.4 Cost Control & Invoicing

- Courier invoices are verified against dispatch logs and PODs before submission to Finance/Admin.
- FM & Admin reviews monthly courier spend by site to identify cost trends or opportunities for consolidation.

6.5 Records & Documentation

- FM & Admin maintains a courier log (per site) capturing date, requester, destination, vendor, cost, and POD status.

7. Approval Matrix & Spend Thresholds

Approval follows a multi-level path: Requester → Site Facility Coordinator / Facility Manager → Department Head, scaled to cost as below.

Spend Level (EGP)	Catering	Courier	Required Approval
Up to 1,000	Routine/standing orders	Standard domestic courier	Site Facility Coordinator / FM & Admin
1,001 – 5,000	Small meeting/event catering	Express or multi-parcel dispatch	Facility Manager
5,001 – 20,000	Larger event catering	high-value courier	Facility Manager + Department Head
Above 20,000	Large-scale/VIP event catering	Bulk or contracted courier arrangement	Department Head

Emergency or after-hours requests may proceed with verbal approval from the Facility Manager; provided written confirmation follows within 1 working day (see Section 9).

8. Site Coordination

This SOP applies uniformly across Head Office and all company sites. Each site designates a Site Facility Coordinator as the local point of contact; the Facility

Assistant Manager retains overall approval and audit responsibility across all locations.

Location	Site Facility Coordinator	Notes
Head Office (HQ)	Senior Site Admin	Primary catering and courier hub; consolidates cross-site vendor arrangements.

9. Exceptions & Emergency Procedures

- Urgent catering (under 24 hours' notice) or urgent courier (same day) may be actioned on verbal approval from the Facility Manager or, in their absence, the most senior available FM & Admin staff member.
- Verbal approvals must be confirmed in writing (email) within 1 working day, referencing the original request.
- Requests from non-approved vendors are permitted only when no approved vendor can meet the requirement and must be documented with justification and retrospective FM & Admin sign-off.
- Any exception is logged in the relevant catering or courier log with an "Exception" flag for later audit review.

10. Non-Compliance & Escalation

- Requests submitted without required approval will not be processed by FM & Admin, except under the Exceptions procedure in Section 9.
- Repeated vendor quality, hygiene, or delivery failures are escalated to the Facility Manager by the Department Head with a recommendation (warn or remove vendor).
- Any suspected misuse of catering or courier services for non-business purposes is reported to the Department Head and, where relevant, HR.

11. Internal and External References

In this section, the references that FM Team follows will be listed. There are two types of references: internal references and external references

11.1 Internal References

- FM SOP
- Karm's policies and regulations
- Other functions' SOPs
- Top management decisions

11.2 External References

- Egyptian code for firefighting
- NFPA codes and standards
- IFMA
- IEEE standards
- ASHRAE standards and guidelines
- ISO standards
- International Plumbing Code (IPC)
- IEC
- Egyptian labor law

12. Facilities DETAILS

12.1 Layouts and Designs

Table 24 - Designs and Layouts

Sites	Locations	Adress
Arkan Mall PV	https://maps.app.goo.gl/9xgHMTyvCg1VzbeY7	Sheikh Zayed City
Orion Factory	https://maps.app.goo.gl/MJ5Yfzww2QBGDRza9	6th October City
Mazar Mall PV	https://maps.app.goo.gl/5MM4geFrWDGSqhWbA	Sheikh Zayed City
C3A	https://maps.app.goo.gl/KSH4hcKaH1C62rXj8	Wahat
Juhaina	https://maps.app.goo.gl/8rwp78BqeJNti2wm7	Wahat
Abu Monkar	https://maps.app.goo.gl/poRM6LSRAFSMvCL96	Abu Monkar - Farafra
DAK-01	https://maps.app.goo.gl/1cH8CkeLUK74FNiR9	Minya
DAK-02	https://maps.app.goo.gl/ikbWsEmuDoNNmGm67	Wadi Elnatroon
Sahl Hashish	https://maps.app.goo.gl/oTNaDEiA7fN6xpYW8	Sahl Hashish
Oasis	https://maps.app.goo.gl/LhUDuJQufds3H2PA7	North Marsa Alam
Equinox	https://maps.app.goo.gl/ci9SA8YZruK4mVCC8	North Marsa Alam
Marsa Shagara	https://maps.app.goo.gl/Csp6gukoeFd2jrAAA	North Marsa Alam
Lahmy Bay	https://maps.app.goo.gl/gbmVi3wriqAhBCYh8	South Marsa Alam
Wadi Lahmy Azure	https://maps.app.goo.gl/WTGJVasbmGQXXnyz8	South Marsa Alam
Nakari	https://maps.app.goo.gl/WN8xXUkMfHqCtjkBA	South Marsa Alam
Wadi Lahami	https://maps.app.goo.gl/VZFEE83Athr6kBfp8	South Marsa Alam
District 5	https://maps.app.goo.gl/mTSnsVkefqyHkScB8?g_st=aw	New Cairo

13. Recommendations

13.1 Computerized Maintenance Management System - CMMS

A CMMS is a software tool used by maintenance planners, schedulers, and technicians to manage maintenance activities and increase the reliability and lifespan of assets and equipment.

CMMS will help FM Team to work efficiently and to track the daily activities. CCMS will help FM Team to:

- Work order management
- Resource and labor management / scheduling
- Asset registry
- Condition monitoring
- Predictive maintenance
- Reporting and analytics
- Parts and inventory management

14. Checklists Templates

FM Team uses some forms templates to define the status of assets maintenance, utilities & manpower performance in this chapter, all FM's checklist templates will be listed for visibility.

14.1 FM Technicians Daily Report

Table 25 - FM Technicians Daily Report

سجل العمل اليومي للفني

Technician Daily Work Log

ادارة المرافق - كارم سولار: سجل العمل الميداني والصيانة اليومي

* 1. التاريخ

* 2. اسم الفني	* 3. الموقع
------------------------------------	---------------------------------

*** 4. الوردية**

☐ صباحية	☐ مسائية	☐ ليلية
---------------------------------	---------------------------------	--------------------------------

*** 5. وقت الحضور / وقت الانصراف**

*** 6. الحضور والاستعداد**

- ☐ الحضور في الموعد المحدد
- ☐ ارتداء معدات الحماية الشخصية كاملة
- ☐ فحص الأدوات والمعدات قبل الاستخدام

☐ الاطلاع على قائمة المهام اليومية

7. المهام المنجزة اليوم (الموقع/الأصل، الوصف، النوع، الوقت) *

8. المواد / قطع الغيار المستخدمة (الاسم، الكمية، المصدر)

9. المشاكل والأعطال والملاحظات (وصف المشكلة، السبب إن وجد، الإجراء المتخذ)

10. حالة حل المشكلة (إن وجدت)

- ☐ تم الحل في الموقع
- ☐ تم التصعيد إلى المشرف
- ☐ يلزم زيارة متابعة
- ☐ تم طلب قطع غيار / مواد

11. السلامة والنظافة العامة

- ☐ منطقة العمل نظيفة وآمنة
- ☐ لا توجد حوادث سلامة خلال الوردية
- ☐ تم الإبلاغ عن المخاطر (إن وجدت)
- ☐ تم إرجاع/تخزين المعدات بشكل صحيح

12. ملاحظات عامة

14.2 Daily Utility Inspection Checklist

Table 26 - Daily Utility Inspection Checklist

قراءة عداد المياه و الكهرباء

Water & Electricity Meter Reading

يرجى تسجيل قراءات العدادات الشهرية لكل دور، بالإضافة إلى بيانات عداد المياه.

قراءات عدادات الكهرباء

الدور	قراءة العداد	باقي الفلوس في العداد
الدور الثالث		
الدور الرابع		
الدور الخامس		
الدور السابع		

عداد المياه

9. قراءة عداد المياه 1 الشهرية

10. تكلفة فاتورة المياه

14.3 FM HK Checklist**Table 27 - HK Checklist****تقييم أعمال النظافة****H.K Feedback (Housekeeping)**

جميع الأسئلة إجبارية.

1. مشرف كارم للطاقة الشمسية *

☐ سيد جمعه	☐ حسين كمال	☐ سماح سيد
-----------------------------------	------------------------------------	-----------------------------------

م	البند	التقييم (1 إلى 5)	غير ذلك
2	نظافة المطبخ	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
3	نظافة الأرضية	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
4	نظافة الكراسي والكنب والمكاتب الخشبية	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
5	نظافة الزجاج	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
6	نظافة التراسات	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
7	نظافة الحمامات	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
8	نظافة الحوائط	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
9	نظافة التكييفات، الإنارة، طفايات الحريق، الكاميرات	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	
10	نظافة الأسقف	5 ☐ 4 ☐ 3 ☐ 2 ☐ 1 ☐	

11. نظافة فلاتر التكييفات *

غير ذلك: _____	☐ لا	☐ نعم
----------------	-----------------------------	------------------------------

12. نظافة الكنب والكراسي *

غير ذلك: _____	☐ لا	☐ نعم
----------------	-----------------------------	------------------------------

13. تعليقات أخرى

14.4 FM Stock Consumption Report

Table 28 - Stock Consumption Report



استهلاك المخزون الإداري Admin Stock Consumption

يرجى تعبئة هذا النموذج لتسجيل استهلاك المخزون الإداري لموقعك.

1. الموقع *

HQ ☐	Sand ☐
-----------------------------	-------------------------------

م	المنف	الكمية المستهلكة (اختار رقم)	غير ذلك
2	زجاجة لبن كامل الدسم	1 ☐ 2 ☐ 3 ☐ 4 ☐ 5 ☐	_____
3	زجاجة لبن خالي الدسم	1 ☐ 2 ☐ 3 ☐ 4 ☐ 5 ☐	_____
4	كيس سكر	1 ☐ 2 ☐ 3 ☐ 4 ☐ 5 ☐	_____
5	كيس بن فاتح سادة	1 ☐ 2 ☐ 3 ☐ 4 ☐ 5 ☐	_____
6	كيس بن فاتح محوج	1 ☐ 2 ☐ 3 ☐ 4 ☐ 5 ☐	_____
7	كيس بن وسط محوج	1 ☐ 2 ☐ 3 ☐ 4 ☐ 5 ☐	_____

م	الصف	الكمية المستهلكة (اختار رقم)	غير ذلك
8	كيس بن غامق محوج	1□ 2□ 3□ 4□ 5□	
9	باكت شاي فتلہ	1□ 2□ 3□ 4□ 5□	
10	باكت شاي اخضر	1□ 2□ 3□ 4□ 5□	
11	باكت كركديه فتلہ	1□ 2□ 3□ 4□ 5□	
12	باكت ينسون فتلہ	1□ 2□ 3□ 4□ 5□	
13	باكت نعناع فتلہ	1□ 2□ 3□ 4□ 5□	
14	باكت قرفه فتلہ	1□ 2□ 3□ 4□ 5□	
15	باكت جنزيب فتلہ	1□ 2□ 3□ 4□ 5□	
16	قارورة مياه	1□ 2□ 3□ 4□ 5□	
17	باكت مناديل سحب	1□ 2□ 3□ 4□ 5□ 6□ 7□ 8□ 9□ 10□	
18	باكت مناديل مكتب فاين	1□ 2□ 3□ 4□ 5□ 6□ 7□ 8□ 9□ 10□	
19	بكرة مناديل	1□ 2□ 3□ 4□ 5□ 6□ 7□ 8□ 9□ 10□	
20	برطمان نسكافيه	1□ 2□ 3□ 4□ 5□	
21	عسل ابيض امتنان	1□ 2□ 3□ 4□ 5□	
22	زجاجة مياه 300مل	1□ 2□ 3□ 4□ 5□ 6□ 7□ 8□ 9□ 10□	
23	رزمة ورق A4	1□ 2□ 3□ 4□ 5□	
24	رزمة ورق A3	1□ 2□ 3□ 4□ 5□	
25	قلم marker	1□ 2□ 3□ 4□ 5□	
26	بشورة	1□ 2□ 3□ 4□ 5□	

م	الصف	الكمية المستهلكة (اختار رقم)	غير ذلك
27	القطر	1□ 2□ 3□ 4□ 5□	_____
28	استيكس نوت (أسهم)	1□ 2□ 3□ 4□ 5□	_____
29	استيكس نوت (مربعات)	1□ 2□ 3□ 4□ 5□	_____
30	قلم جاف	1□ 2□ 3□ 4□ 5□	_____
31	فايل شفاف	1□ 2□ 3□ 4□ 5□ 6□ 7□ 8□ 9□ 10□	_____
32	فايل A4 ابيض	1□ 2□ 3□ 4□ 5□	_____
33	فايل A3 ابيض	1□ 2□ 3□ 4□ 5□	_____
34	بطاريه AAA	1□ 2□ 3□ 4□ 5□	_____
35	بطاريه AA	1□ 2□ 3□ 4□ 5□ 6□	_____
36	باكت دبابيس	1□ 2□ 3□ 4□ 5□	_____
37	راس تحويل من ثلاثي الي ثنائي	1□ 2□ 3□ 4□ 5□	_____
38	مشترك متعدد المخارج	1□ 2□ 3□ 4□ 5□	_____
39	كفرومه	1□ 2□ 3□ 4□ 5□	_____
40	زجاجة معطر جو	1□ 2□ 3□ 4□ 5□	_____
41	زجاجة ديتول مطبخ	1□ 2□ 3□ 4□ 5□	_____
42	زجاجة ديتول حمام	1□ 2□ 3□ 4□ 5□	_____
43	زجاجة hand soap	1□ 2□ 3□ 4□ 5□	_____
44	زجاجة body lotion	1□ 2□ 3□ 4□ 5□	_____

45. تعليقات أخرى

14.5 Vendor Evaluation Template

Table 29 - Vendor Evaluation Template

Vendor Evaluation		
Vendor Name		
Type of service		
	Response time	
	Commitment to FM-HSE	
	Timeline	
	Quality	
	Handover	
	Warranty	

14.6 Facility Handover

KARMSOLAR

SITE HANDOVER CHECKLIST

Landlord-to-Facility-Team Handover Record

SECTION 1 — GENERAL INFORMATION

Site Name / Code:

Handover Date:

Landlord Name:

Landlord Contact No.:

Facility Team Representative:

FM Rep. Contact No.:

Previous Occupant (if any):

Handover Reference / Ref. No.:

SECTION 2 — UTILITIES & METER READINGS

Utility / Meter	Reading at Handover	Meter Serial No.	Photo Taken
Electricity meter			☐ Yes
Water meter			☐ Yes
Gas meter (if applicable)			☐ Yes
Generator hour-meter			☐ Yes

☐ Utility accounts already registered in landlord's name ☐ Outstanding utility bills at handover

☐ Emergency shut-off valves/breakers identified & labeled

SECTION 3 — PHYSICAL CONDITION ASSESSMENT

Item	Excellent	Good	Fair	Poor	Notes
Walls / paint	☐	☐	☐	☐	
Flooring	☐	☐	☐	☐	
Ceiling	☐	☐	☐	☐	
Windows & doors	☐	☐	☐	☐	
Plumbing (leaks/blockages)	☐	☐	☐	☐	
HVAC / AC units	☐	☐	☐	☐	
Electrical fittings & sockets	☐	☐	☐	☐	

Item	Excellent	Good	Fair	Poor	Notes
Lighting fixtures	☐	☐	☐	☐	

Additional Condition Notes

☐ Photographs of all rooms/areas attached or uploaded separately

SECTION 4 — KEYS & ACCESS
No. of Keys Received:

Key / Access Card Type(s):

No. of Access Cards Received:

Master Key Location:

☐ Access codes / alarm codes provided in writing

☐ Spare keys handed over

☐ All keys tested and confirmed functional

☐ Access list of authorized personnel updated

SECTION 5 — EQUIPMENT, FIXTURES & SAFETY ITEMS

Fixtures / furniture left by landlord (list below)

Safety Equipment

- | | |
|--|--|
| ☐ Fire extinguishers present and within validity date | ☐ Smoke detectors present and functioning |
| ☐ Emergency lighting functioning | ☐ Fire exit signage present and visible |
| ☐ First aid kit present and stocked | ☐ Emergency assembly point identified |

Any equipment malfunctioning or missing at handover

SECTION 6 — DOCUMENTS RECEIVED FROM LANDLORD

- | | |
|--|---|
| ☐ Lease / contract copy | ☐ Building floor plan / layout |
| ☐ Civil Defense / fire safety certificate | ☐ Previous maintenance records |
| ☐ Insurance documents | ☐ Utility account documents |
| | ☐ As-built drawings (if available) |

SECTION 7 — HANDOVER DECISION & SIGN-OFF**Handover Status:**☐ Accepted with no issues☐ Accepted with noted issues (see notes below)☐ Not accepted — pending landlord action**Remarks / Conditions of Acceptance**

Signature**Landlord / Site Owner****Name:** _____**Date:** __________
Signature**Facility Team Representative****Name:** _____**Date:** _____

15. Definitions and Abbreviations

In this section, definitions and abbreviations are listed:

Table 30 - Definitions and Abbreviations

Abbreviation	Description
FM	Facility Management
IFMA	International Facility Management Association
FM Ticket	Facility Management Ticket
PR Ticket	Purchase Requisition Ticket
FIN Ticket	Finance Ticket
SOP	Standard Operating Procedures
DN	Delivery Note
E-Invoice	Electronic Invoice
HSE	Health, Safety & Environment
WHT	Withholding Tax
POP	Proof of Payment
DOA	Delegation of Authorities
VAT	Value-Added Tax
BOQ	Bill of Quantity
PPM	Planned Preventative Maintenance
KPI	Key Performance Index
Specs	Specifications
PTW	Permit to Work
OT	Overtime
PO	Purchasing Order
TAT	Turnaround Time
HOD	Head of Department
PMI	Project Management Institute
REV Ticket	Finance Revenue Ticket
NFPA	National Fire Protection Association
IEEE	Institute of Electrical and Electronics Engineers
ASHRAE	American Society of Heating, Refrigeration, and Air-conditioning Engineers
ISO	International Standards Organization
IPC	International Plumbing Code
IEC	International Electrotechnical Commission
SFM	Soft Facility Management

Abbreviation	Description
HK	Housekeeping
PC	Pest Control
HC	Headcount
SLA	Service-Level Agreement
MEP	Mechanical, Electrical & Plumbing
MHE	Material Handling Equipment
ZCV	Zone Control Valve
FHC	Fire Hose Cabinet
FF	Firefighting
FA	Fire Alarm
RT	Reach Truck
POC	Point of Contact
PPE	Personal Protective Equipment
MSRA	Method statement and Risk Assessment
TL	Team Leader

16. Change History

SOP no.	Effective Date	Significant Changes	Action By	Previous SOP number.
